

Project Profile

for

Upgrading of Pillar Point Sewage Treatment Works



**Drainage Services Department
The Government of the Hong Kong Special Administrative Region**

TABLE of CONTENT

1 BASIC INFORMATION

1.1 Project Title	1
1.2 Purpose and Nature of the Project	1
1.3 Name of Project Proponent	2
1.4 Location and Scale of the Project	2
1.5 Type of Designated Project Involved	2
1.6 Contact Person	2

2. OUTLINE OF PLANNING AND IMPLEMENTATION PROGRAMME

2.1 Project Offices/Divisions	2
2.2 Project Time Table	3

3. POSSIBLE IMPACTS ON THE ENVIRONMENT

3.1 Project Outline and Preliminary Environmental Review	3
3.2 Possible Environmental Impacts during the Construction Stage	
3.2.1 Air Quality	4
3.2.2 Water Quality	4
3.2.3 Noise	4
3.2.4 Generation of Waste	5
3.2.5 Ecology	5
3.2.6 Visual Impact	5
3.2.7 Traffic Disruption	5
3.3 Possible Environmental Impacts during the Operation Stage	
3.3.1 Air Quality	5
3.3.2 Water Quality	5
3.3.3 Noise	6
3.3.4 Generation of Waste	6
3.3.5 Ecology	6
3.3.6 Visual Impact	7
3.3.7 Storage, Use, Handling, Transport and Disposal of Disinfection Material	7
3.3.8 Risk of Accidents Resulting in Pollution	7
3.3.9 Cumulative Impacts	7

4. MAJOR ELEMENTS OF THE SURROUNDING ENVIRONMENT

4.1 Residential Developments	8
4.2 Industries	8
4.3 Water Courses	8
4.4 Beaches	8
4.5 Marine Park	8

5. ENVIRONMENTAL PROTECTION MEASURES TO BE INCORPORATED IN THE DESIGN OF THE PROJECT

5.1 During the Construction Stage	
5.1.1 Air Quality	9
5.1.2 Water Quality	9
5.1.3 Noise	9
5.1.4 Generation of Waste	10
5.1.5 Ecology	10
5.1.6 Visual Impact	10
5.1.7 Traffic Disruption	10
5.2 During the Operation Stage	
5.2.1 Air Quality	10
5.2.2 Water Quality	11
5.2.3 Noise	11
5.2.4 Generation of Waste	11
5.2.5 Ecology	11
5.2.6 Visual Impact	12
5.2.7 Storage, Use, Handling, Transport and Disposal of Disinfection Material	12
5.2.8 Risk of Accidents Resulting in Pollution	12
5.2.9 Cumulative Impacts	12

LIST OF DRAWING

Drawing No. DPM 0106	- Location Plan of the Upgraded Works of Pillar Point Sewage Treatment Works
Drawing No. DPM 0107	- Upgraded Pillar Point Sewage Treatment Works - Major Elements of the Surrounding Environment

1. BASIC INFORMATION

1.1 Project Title

The title of this project is :

“Upgrading of Pillar Point Sewage Treatment Works” hereinafter referred to as the “Project”.

1.2 Purpose and Nature of the Project

The Project is to expand the sewage treatment capacity and to upgrade the treatment level of the Pillar Point Sewage Treatment Works (PPSTW) in order to cater for the projected ultimate population and planned developments in the Tuen Mun area. This will reduce the pollution loadings to the receiving water, namely the western waters of HKSAR, with a view to contributing to the achievement of water quality objectives set for the receiving waters and to mitigate the adverse impacts of the area’s sewage discharges to aquatic environment.

The key elements of the Project are:

- (a) modify and expand the existing aerated grit channels;
- (b) construct primary treatment units;
- (c) construct sedimentation units;
- (d) construct solid treatment units, including sludge digestors and sludge dewatering facilities;
- (e) construct sludge thickening facilities;
- (f) construct disinfection units;
- (g) modify and expand the existing septic waste reception facilities; and
- (h) modify and expand the existing ancillary facilities including administration building, workshop, laboratory and landscaping works.

1.3 Name of Project Proponent

Project Management Division, Drainage Services Department

1.4 Location and Scale of the Project

The existing PPSTW is located north of the Tuen Mun River Trade Terminal and bounded to the north by Lung Mun Road. The proposed upgrading works will be located on an adjacent land reserved for the extension of the existing PPSTW as shown on Drawing No. DPM 0106.

Upon completion of the Project, the PPSTW can cater for a daily average flow of 241,000 m³/d.

1.5 Type of Designated Project Involved

The Project constitutes a single Designated Project under Schedule 2, Part I, F.1 of the Environmental Impact Assessment Ordinance.

1.6 Contact Person

2. OUTLINE OF PLANNING AND IMPLEMENTATION PROGRAMME

2.1 Project Offices/Divisions

The Project Management Division of the Drainage Services Department will be responsible for the overall planning and implementation of the Project. Consultants will be engaged to

undertake site investigations, environmental impact assessment, design and construction supervision of the Project. Construction will be contracted out.

Operation and maintenance of the completed works will be taken up by Sewage Treatment 1 Division of the Drainage Services Department or a contractor to be employed by Drainage Services Department.

2.2 Project Time Table

The design and construction works of the Project is scheduled to start in 2002 and 2006 respectively. The upgrading works are programmed to have phased completion with phase 1 to be completed in 2008 and phase 2 in 2010 to meet the planned population intake of the major housing development at Tuen Mun Area 54 Phase II.

3. POSSIBLE IMPACT ON THE ENVIRONMENT

3.1 Project Outline and Preliminary Environment Review

The Project comprises:

- (a) expanding the existing PPSTW; and
- (b) upgrading the sewage treatment process by the addition of chemically enhanced primary treatment (CEPT) with disinfection facilities.

To this end, additional sewage treatment and sludge treatment process units will be constructed, and parts of the existing units will be modified.

In the Review of Tuen Mun and Tsing Yi Sewerage Master Plans Final Working Paper WP9 - Final Sewage Treatment and Disposal for Tuen Mun, a Preliminary Environmental Review (PER) of the Project has been conducted to identify the possible impacts to the environment. The PER has concluded that no insurmountable environmental impacts are identified from the construction and operation of the proposed works provided that effective mitigation measures are implemented. It also suggests to have a comprehensive assessment of the potential environmental impacts during the design stage when more information on the proposed works

is available.

3.2 POSSIBLE ENVIRONMENTAL IMPACTS DURING THE CONSTRUCTION STAGE

3.2.1 Air Quality

Gaseous and odour emission will unlikely arise from construction of the Project.

Dust may be generated from some construction activities, mainly earthwork and demolition works. In view of the modest scale of construction, the potential dust impact can be minimized through good construction practices.

3.2.2 Water Quality

Potential water quality concerns during construction of the Project include site run-off and drainage, and discharge of sewage from the construction workforce.

3.2.3 Noise

The construction activities will generate some noise through the use of conventional construction plant and equipment, like air compressors, breakers, etc.

3.2.4 Generation of Waste

Construction of the project will generate some construction and demolition materials (C&DM), including: waste spoil from site clearance and excavation works; construction material such as wood, metal scraps and concrete; chemical waste from maintenance of plant and equipment and general waste from construction workforce.

3.2.5 Ecology

Potential impacts may include the total or partial loss of habitats at both permanent surface structures and temporary construction sites due to land preparation, construction activities and storage of spoil and bulk construction materials. As the proposed site is on a reclaimed land, the ecological impact will be minimal.

3.2.6 Visual Impacts

Visual impacts resulted from the construction activities will be temporary. The presence of construction equipment and stockpiled materials on works site may be a source of visual impacts to nearby sensitive receivers.

3.2.7 Traffic Disruption

The construction of the proposed works may result in impacts on nearby traffic, particularly Lung Mun Road and the entrance to the River Trade Terminal (RTT) site. As the scale of construction works related to the upgrading works is not large, it is anticipated that the impacts on traffic will be minimal.

3.3 POSSIBLE ENVIRONMENTAL IMPACTS DURING THE OPERATION STAGE

3.3.1 Air Quality

The potential odour sources in the PPSTW are the sludge treatment units and the sludge and screenings handling facilities. Moreover, prolonged storage of the screenings and grit in the storage skips of the screening compactors and dewatering facilities may also create odour problem.

3.3.2 Water Quality

The quality of the treated effluent discharging from the existing PPSTW is within the discharge limits specified in the current discharge licence standards. The upgrading works

propose to extend the PPSTW to cope with increased sewage flows and to provide a higher level of treatment. The upgraded PPSTW will provide CEPT plus disinfection, which will decrease the suspended solids, biochemical oxygen demand and E. coli concentrations in the treated effluent by a minimum of 70%, 55% and 99.9%, respectively.

The PPSTW will be upgraded to cater for the increased flows, thus increasing the discharges to the receiving water. However, owing to the greater extent of treatment improvement, the future total loads of pollutants to the receiving waters will therefore be reduced.

3.3.3 Noise

The sewage/sludge pumps and the ventilation fans of ventilation systems are potential noise sources during operation of the PPSTW.

3.3.4 Generation of Waste

The provision of CEPT at the upgraded PPSTW will generate more sludge than is presently the case. The PPSTW currently generates approximately 3-4 m³/d of sludge from the coarse and fines screening and grit removal. At the upgraded PPSTW, sludge will be thickened and dewatered prior to anaerobic digestion to reduce the volumes of sludge produced, where the total sludge volume produced is estimated at 91 m³/d, which is a considerable increase over that currently generated. It is therefore considered that the potential impact related to handling, transportation and disposal of the waste during operational phase would be a concern.

3.3.5 Ecology

By the same reason as mentioned in paragraph 3.3.2, adverse impact on marine ecology would be unlikely as the total future loads of pollutants to the receiving waters would be reduced.

3.3.6 Visual Impact

The project is located within a developed area with no residential establishments in the close proximity of the site .

3.3.7 Storage, Use, Handling, Transport and Disposal of Disinfection Material

The Project will explore various disinfection methods to improve the bacterial concentration of the effluent before the effluent is discharged to the receiving waters. There is a potential impact due to storage, use, handling, transport and disposal of the disinfection material.

3.3.8 Risk of Accidents Resulting in Pollution

The accidental leakage of the submarine outfall and the emergency breakdown of the PPSTW could potentially pollute the receiving water body.

3.3.9 Cumulative Impacts

The existing San Wai Sewage Treatment Works will be expanded and upgraded with scheduled completion in early 2008. There is potential cumulative impact as the effluent from both the San Wai Sewage Treatment Works and the PPSTW are discharged into the Urmston Road.

4. MAJOR ELEMENTS OF THE SURROUNDING ENVIRONMENT

The following is to outline those existing and planned sensitive receivers and the sensitive parts of the natural environment which may be affected by the Project. The locations of the sensitive receivers in concern are shown on the Drawing No. DPM 0107.

4.1 Residential Developments

The PPSTW is located at the southern coast of the western New Territories. The area surrounding the PPSTW is largely unpopulated, and the proposed site of the Project is located within a reserved area next to the existing compounds, surrounding areas belong to various government agencies. Tuen Mun Town Centre is located approximately 15 km north-east of the PPSTW and the closest residential developments, being Butterfly Estate and other residential estates, are located approximately 2 km north-east of the Project site.

4.2 Industries

The China Light & Power Tap Chek Kok Power Station is located approximately 2 km west of the PPSTW.

4.3 Water Courses

The Urmston Road, which is the major marine navigation channel from Hong Kong waters to the Pearl River, is located at the south-western part of the PPSTW.

4.4 Beaches

The nearest gazetted beach is Butterfly Beach which is located approximately 1 km east of the PPSTW. Other gazetted beaches in the area include : Castle Peak Beach, Kadoorie Beach, Cafeteria New Beach and Cafeteria Old Beach which are all located east of Butterfly Beach. Lung Kwu Upper Beach and Lung Kwu Lower Beach, which are non-gazetted beaches, are located about 2.5 km north-west of the PPSTW

4.5 Marine Park

Sha Chau and Lung Kwu Chau Marine Park is located appropriate 4 km west of the PPSTW

5. ENVIRONMENTAL PROTECTION MEASURES TO BE INCORPORATED IN THE DESIGN OF THE PROJECT

5.1 During the Construction Stage

5.1.1 Air Quality

Air quality impacts during construction, which arises mainly from dusts will be minimised by the adoption of proper working methods of dust suppression, including: wetting of structures to be broken down before the demolition works; water spraying; covering of scaffolding with plastic sheet cover; controlling dropping heights of excavated materials; wetting and covering of materials for transportation by trucks; shielding of stockpile materials; and installation of wheel washing facilities. Relevant clauses will be incorporated into the construction contract.

5.1.2 Water Quality

The construction contract will incorporate provisions for removal of sand and debris from site run-off before the run-off can be discharged outside the Project site. Contractors will also be required, under the contract specifications, to ensure that site management is optimised and that the deposit of any solid materials, litter or wastes (solid and liquid) does not occur in drainage channels and all fuel tanks and store areas are provided with locks and are located within secondary containment.

In cases sewerage connections to existing sewers are not available, portable toilets will be provided to collect sewage generated from the construction workforce and arrangements will be made with a licensed contractor for proper disposal of night soil.

5.1.3 Noise

The contractors for the works will have to comply with the provisions of the Noise Control Ordinance.

5.1.4 Generation of Waste

Although the quantity of the waste to be generated during the construction phase is expected to be small, provisions in line with the prevailing policy will be made in the construction contract for the contractor to reuse, recycle construction waste materials and to minimise the generation of them. Good waste management practices will be implemented to ensure proper handling and disposal of waste.

5.1.5 Ecology

Pollution control measures will be implemented to alleviate the ecological impacts arising from dust and noise generated by the construction activities.

5.1.6 Visual Impact

Hoarding will be erected at the site boundary to minimize the visual impact due to construction activities.

5.1.7 Traffic Disruption

Temporary traffic arrangement measures including management of transportation of materials and equipment will be undertaken to minimise traffic impacts.

5.2 During The Operation Stage

5.2.1 Air Quality

Odour impact assessment will be conducted during the design of the Project to identify the impacts to sensitive receptors in the Project setting. Where necessary, mitigation measures such as enclosure of odour sources and odour removal units will be installed as part of the upgrading works. Air from the pump sumps, sludge dewatering building and the sludge thickeners will be directed to the odour removal unit for treatment.

5.2.2 Water Quality

Water quality assessment will be conducted during the design of the Project to analyze the impacts to the nearby sensitive receivers due to the additional discharge from PPSTW into the Urmston Road. Nevertheless, the Project will result in a higher standard of the treated effluent. Therefore, the long-term water quality of the Urmston Road will be improved after the Project is commissioned.

5.2.3 Noise

Noise impact assessment will be conducted during the design of the Project to identify the impacts to sensitive receivers in the Project setting. The location of noise sources such as ventilation opening will be located away from noise sensitive receivers where possible. It is also proposed that as part of the upgrading works, air-cooled noise enclosures or internal building sound proofing measures will be installed to reduce noise generated from facilities such as the blower house and the pump motor houses.

5.2.4 Generation of Waste

The screening and sludge handling facilities will be expanded and constructed as part of the Project to handle the increased amount of solid wastes generated from the sewage treatment processes. Disposal options for the increased quantities of sludge will be explored during the detailed EIA so that off-site impacts are minimised.

5.2.5 Ecology

Ecological impact assessment will be conducted during the design of the Project to analyze the impacts to the marine ecology, in particular the Chinese White Dolphins due to the additional discharge from PPSTW into the Urmston Road. Nevertheless, the Project will result in a higher standard of the treated effluent. Therefore, the long-term ecology of the Urmston Road will be improved after the Project is commissioned.

5.2.6 Visual Impact

Aesthetic consideration will be input in the Project design to enhance the appearance of new constructions and landscape planning will be undertaken to enhance the general outlook of the PPSTW.

5.2.7 Storage, Use, Handling, Transport or Disposal of Disinfection Material

The pollution concern is one of the major factors in selecting the disinfection methods in the EIA study. Procedures and practices controlling the storage, use, handling, transport and disposal of the material will be formulated in the EIA study.


5.2.8 Risk of Accidents Resulting in Pollution

Routine monitoring and maintenance of the pipeline would be carried out. Measures such as dual power supply and standby generators will be explored and emergency action plan will be formulated during the EIA study in the event of a breakdown leading to emergency discharge of the incoming sewage.

5.2.9 Cumulative Impacts

All the environmental protection measures as described in Sections 5.2.1 to 5.2.8 will be assessed taking due consideration of the cumulative impacts due to the operation of the San Wai Sewage Treatment Works.


END OF TEXT

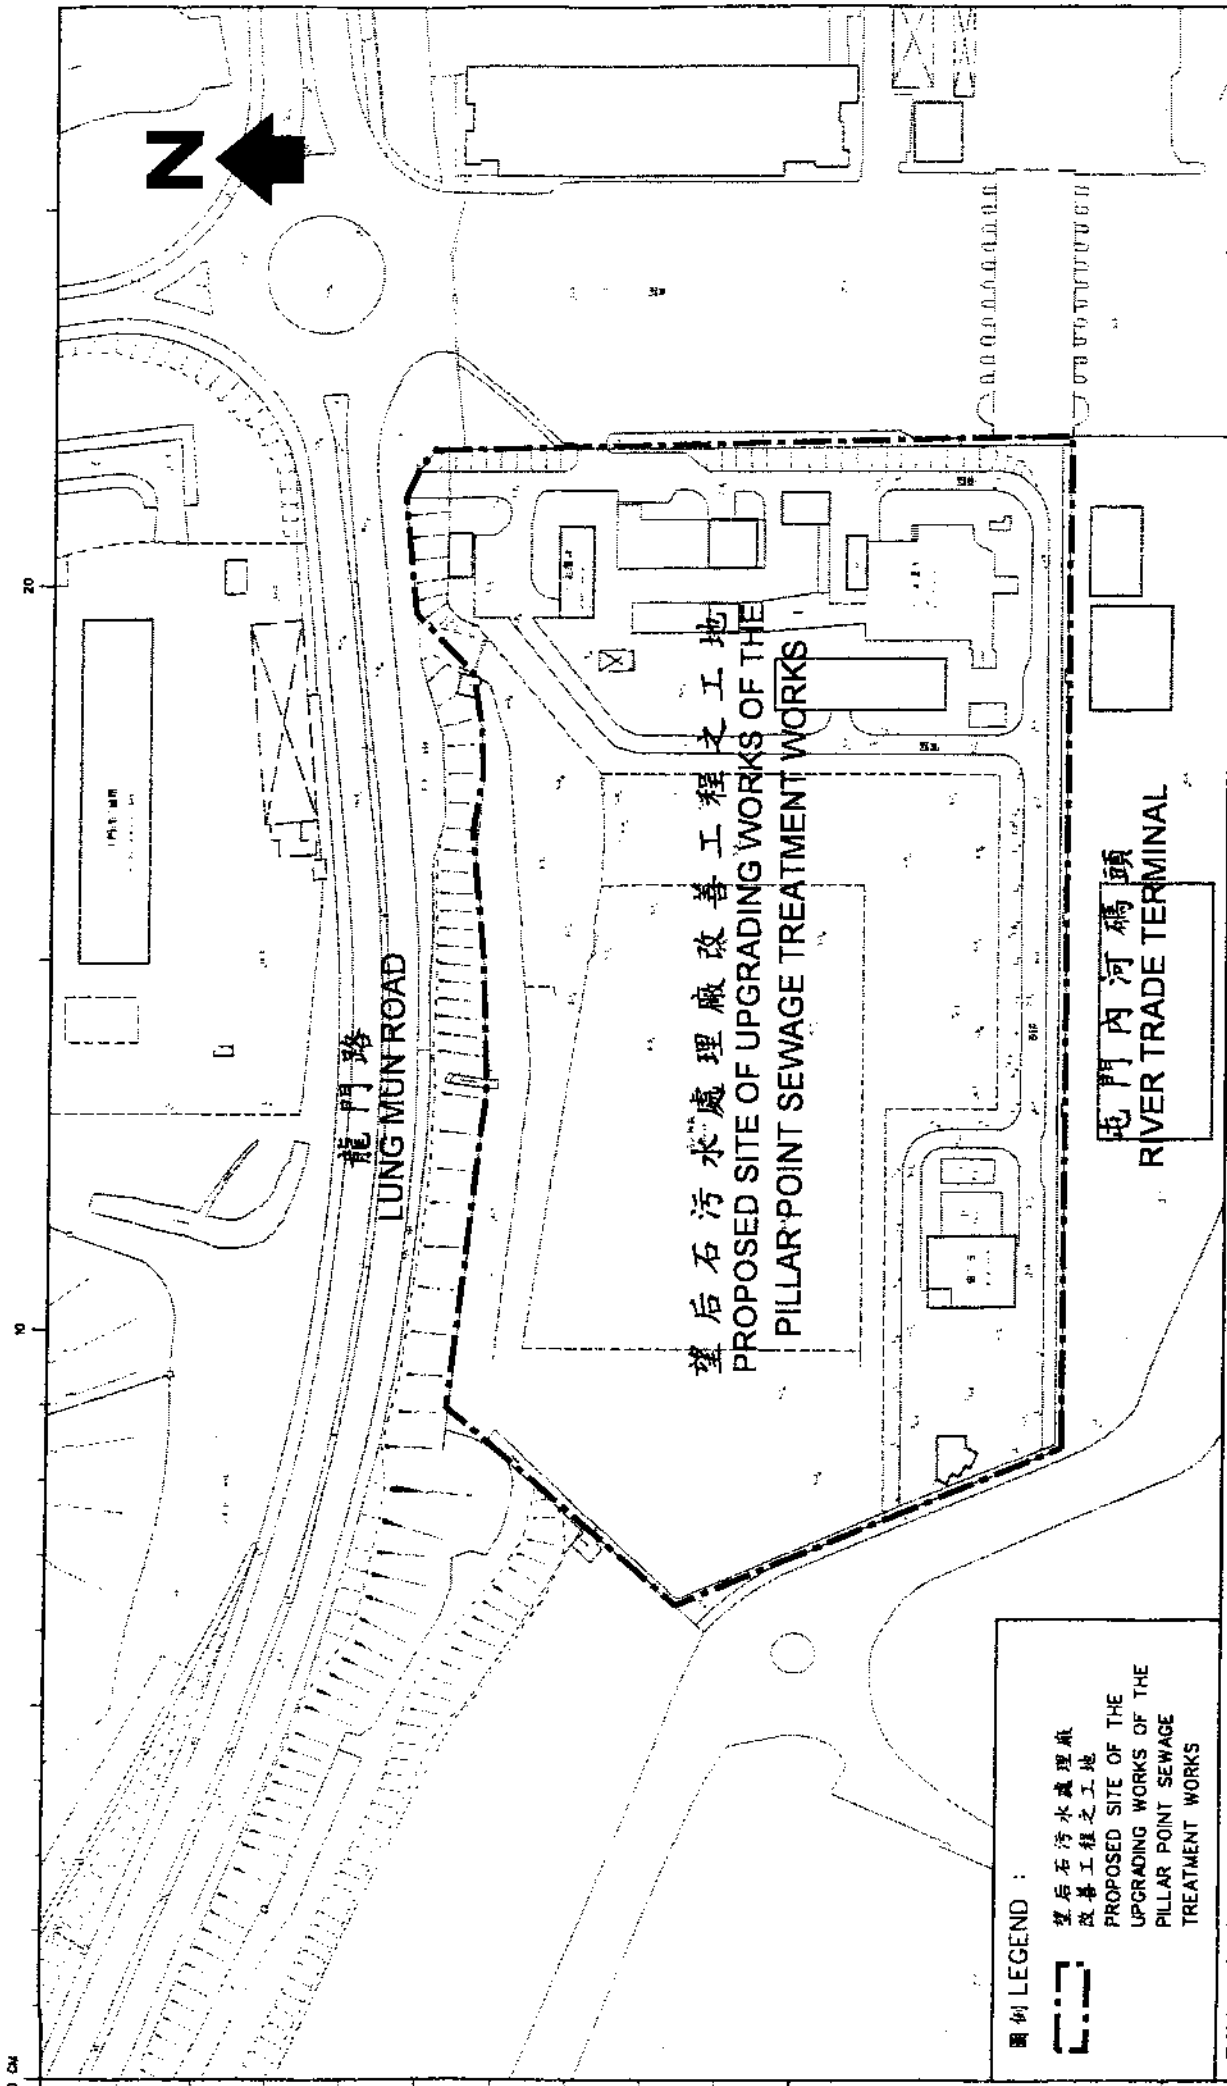


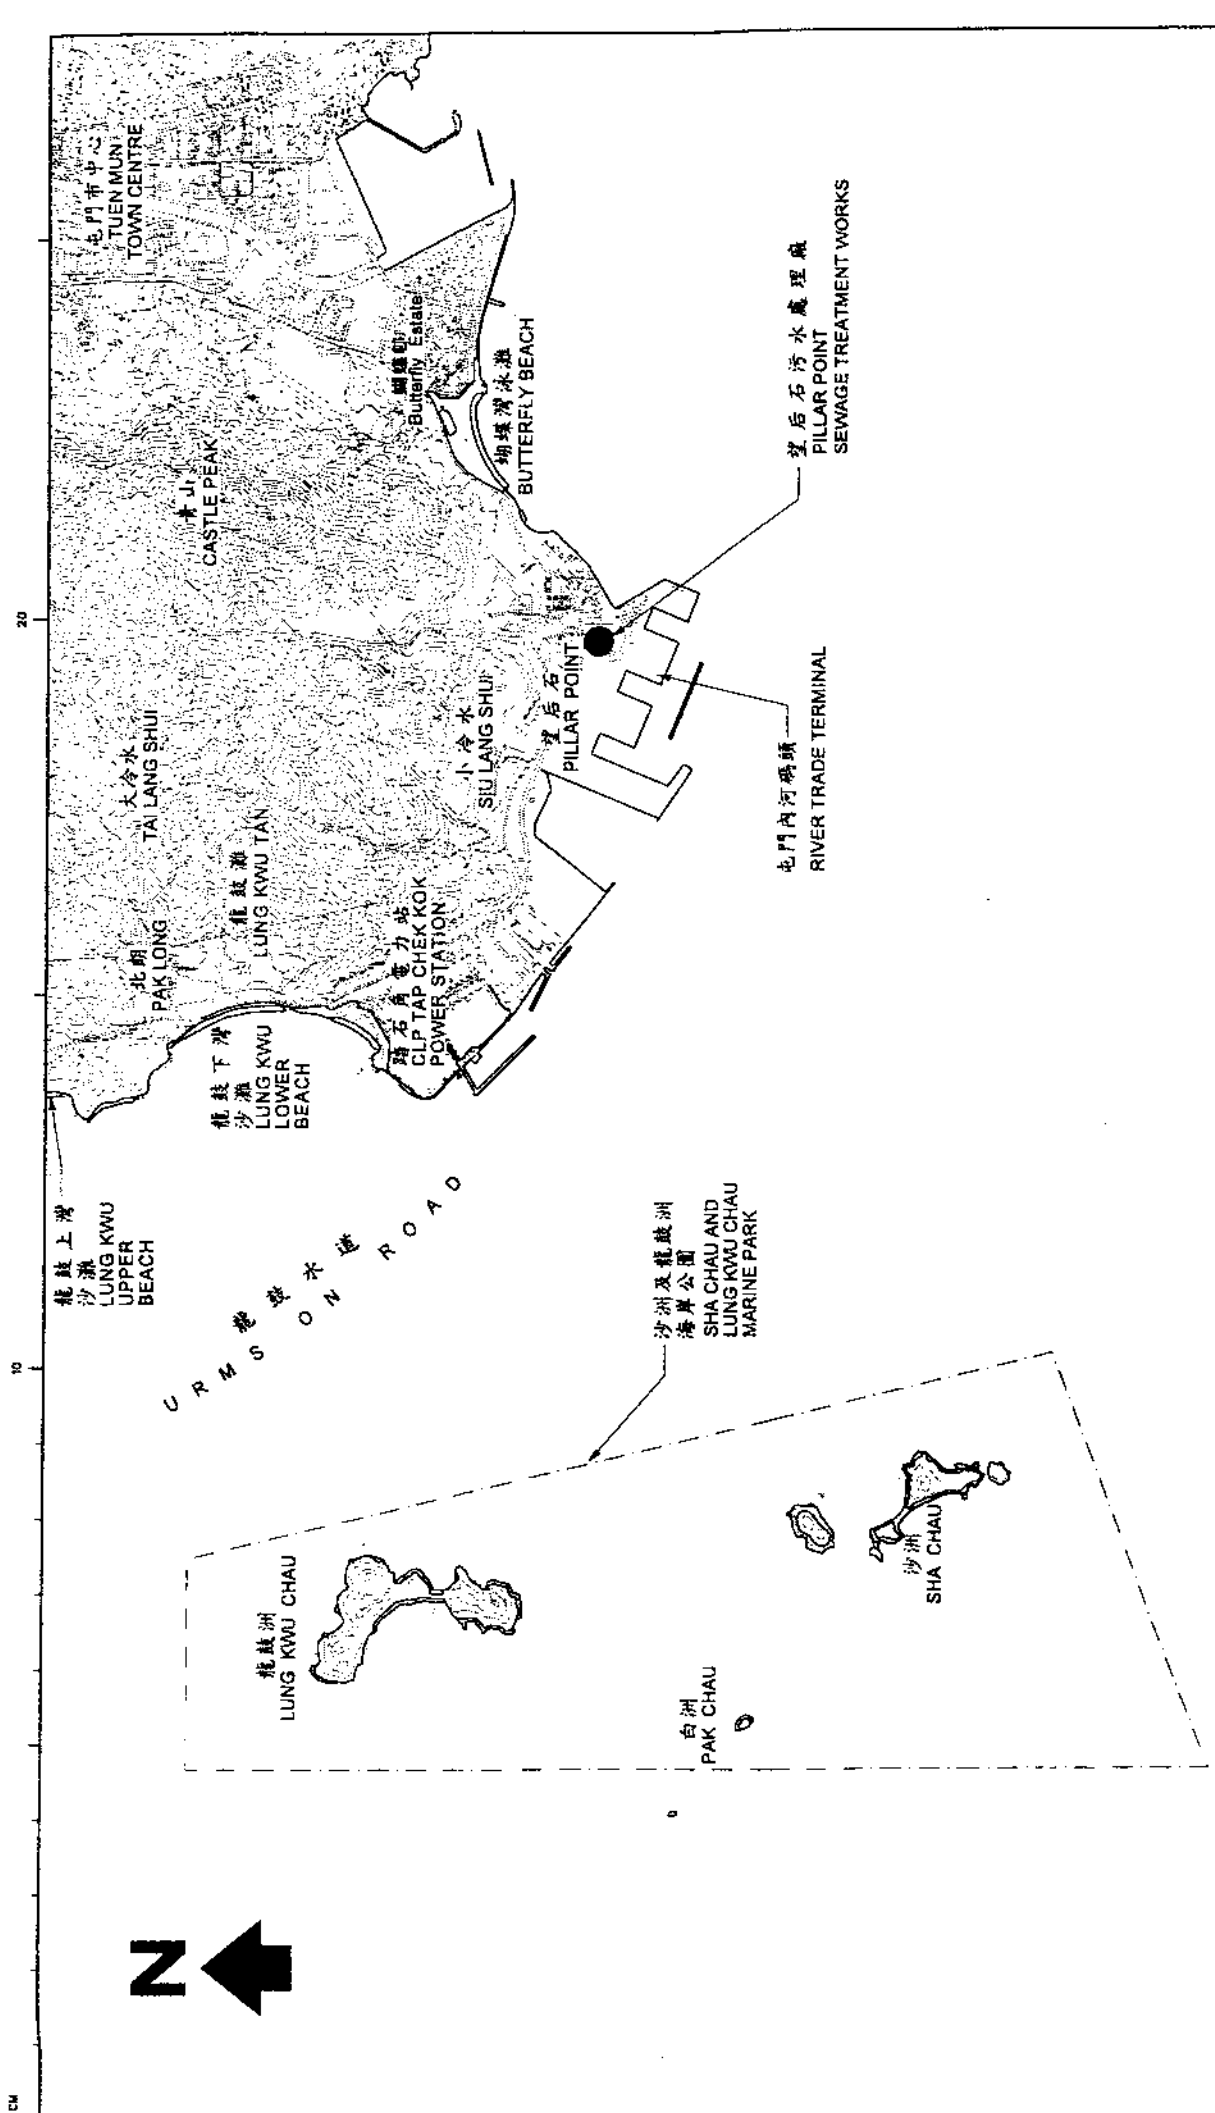
望后石污水處理廠改善工程之工地
 PROPOSED SITE OF UPGRADING WORKS OF THE
 PILLAR POINT SEWAGE TREATMENT WORKS

屯門內河碼頭
 RIVER TRADE TERMINAL

龍門路
 LUNG MUN ROAD

圖例 LEGEND :
 望后石污水處理廠改善工程之工地
 PROPOSED SITE OF THE UPGRADING WORKS OF THE PILLAR POINT SEWAGE TREATMENT WORKS

圖則名稱 drawing title 望后石污水處理廠改善工程之工地 PROPOSED SITE OF THE UPGRADING WORKS OF THE PILLAR POINT SEWAGE TREATMENT WORKS		繪圖 drawn K.P. LO		圖則編號 drawing no. DPM 0106		比例 scale 1:2000	
日期 date 17.10.01		簽名 SIGNED		保留版權 COPYRIGHT RESERVED		香港特別行政區政府渠務署 DRAINAGE SERVICES DEPARTMENT GOVERNMENT OF THE HONG KONG SPECIAL ADMINISTRATIVE REGION	
日期 date 19.10.01		簽名 SIGNED		日期 date 17.10.01			
日期 date 23.10.01		簽名 SIGNED		日期 date 23.10.01			
校核 checked C.S. CHENG		工程管理部 PROJECT MANAGEMENT DIVISION					
批准 approved T. YU							
部門 office PROJECT MANAGEMENT DIVISION							



圖則名稱 drawing title		圖則編號 drawing no.		比例 scale	
望后石污水處理廠改善工程 - 周圍環境主體 UPGRADING OF PILLAR POINT SEWAGE TREATMENT WORKS - MAJOR ELEMENTS OF THE SURROUNDING ENVIRONMENT		DPM0107		1:35,000	
繪圖 drawn	SIGNED	K.P. LO	日期 date	18.10.01	
核對 checked	SIGNED	C.S. CHENG	日期 date	18.10.01	
批准 approved	SIGNED	T.YU	日期 date	23.10.01	
部門 office	工程管理部 PROJECT MANAGEMENT DIVISION				
保留版權 COPYRIGHT RESERVED 香港特別行政區政府渠務署 DRAINAGE SERVICES DEPARTMENT GOVERNMENT OF THE HONG KONG SPECIAL ADMINISTRATIVE REGION					
