Activity ID	Activity Description	Work Days	Cal ID	Early Start	Early Finish
Construction Phase					
1130	Site Preparation & Mobilization	30	2	27AUG03	30SEP03
1140	Environmental Baseline Survey, Test, Reporting	48	2	27AUG03	21OCT03
1150	Preparation and Submission of Temp. Works Design	473	2	27AUG03	28FEB05
1160	Maintenance Dredging for Mai Po Gei Wai	106	2	01JUL03*	31OCT03
1170	Maintenance Dredging for Mai Po Gei Wai	78	2	01APR04*	30JUN04
1180	AMO Rescue Excavation at Land side	80	2	27AUG03	27NOV03
1190	Construct Haul Road	52	2	22OCT03	20DEC03
1200	Formation of Precasting Yard	82	2	27AUG03	29NOV03
1210	Fabricate Precast Segments	391	2	01DEC03	28FEB05
1220	Temporary Access Bridge from Shoreline	300	2	22OCT03	05OCT04
1230	Temporary Access Bridge from other end	300	2	22OCT03	05OCT04
1240	Piles, Pilecaps & Piers in Intertidal Area	240	2	08DEC03	11SEP04
1250	Piles, Pilecaps & Piers on Land side	96	2	13SEP04	01JAN05
1260	Piles, Pilecaps & Piers in Subtidal Area 1	288	2	22OCT03	21SEP04
1270	Piles, Pilecaps & Piers in Subtidal Area 2	308	2	08DEC03	30NOV04
1280	Diversion of CLP Overhead Power lines (By others	106	2	22OCT03	21FEB04
1290	Erect Deck Travellers/Launching Gantries	26	2	01MAY04	31MAY04
1300	Bridge Deck	280	2	01JUN04	22APR05
1310	Cable-stayed Bridge Foundations	165	2	22OCT03	30APR04
1320	Cable-stayed Bridge Tower	313	2	01MAY04	30APR05
1330	Cable-stayed Bridge Back-spans	157	2	01MAY04	30OCT04
1340	Cable-stayed Bridge Main Span	181	2	01NOV04	30MAY05
1350	Bridge Roadworks and Installation of Utilities	260	2	01OCT04	30JUL05
1360	Allowance for Inclement Weather	79	2	01AUG05	31OCT05
1370	Award of TCSS Contract	0	2	15OCT04	
1380	TCSS: Contractor's Design Preparation	60	2	15OCT04	23DEC04
1390	TCSS: Contractor's Design Submission	0	2		23DEC04
1400	TCSS: Submission Review/Revision	60	2	24DEC04	03MAR05
1410	TCSS: Design Approval	0	2		03MAR05
1420	TCSS: Equipment Procurement	158	2	04MAR05	03SEP05
1430	TCSS: Access to Civil Provision	0	2	25AUG05	
1440	TCSS: Install CCTV & LCS and On-site Testing	55	2	25AUG05	27OCT05
1450	TCSS: Other TCSS Installation & On-site Testing	84	2	25AUG05	30NOV05
1460	TCSS: Assist in Sys Integration/Acceptance Test	56	2	28OCT05	31DEC05
1470	Road Opening	0	3		31DEC05
1480	TCSS: Assist in Operability Test	50	2	02JAN06	28FEB06
Finalisation					
1490	Establishment Works and Maintenance Period	313	2	01NOV05	31OCT06
1500	Finalise - Account Finalization	731	3	01MAR06	29FEB08
1510	Finalise - Deletion from PWP	0	3		29FEB08

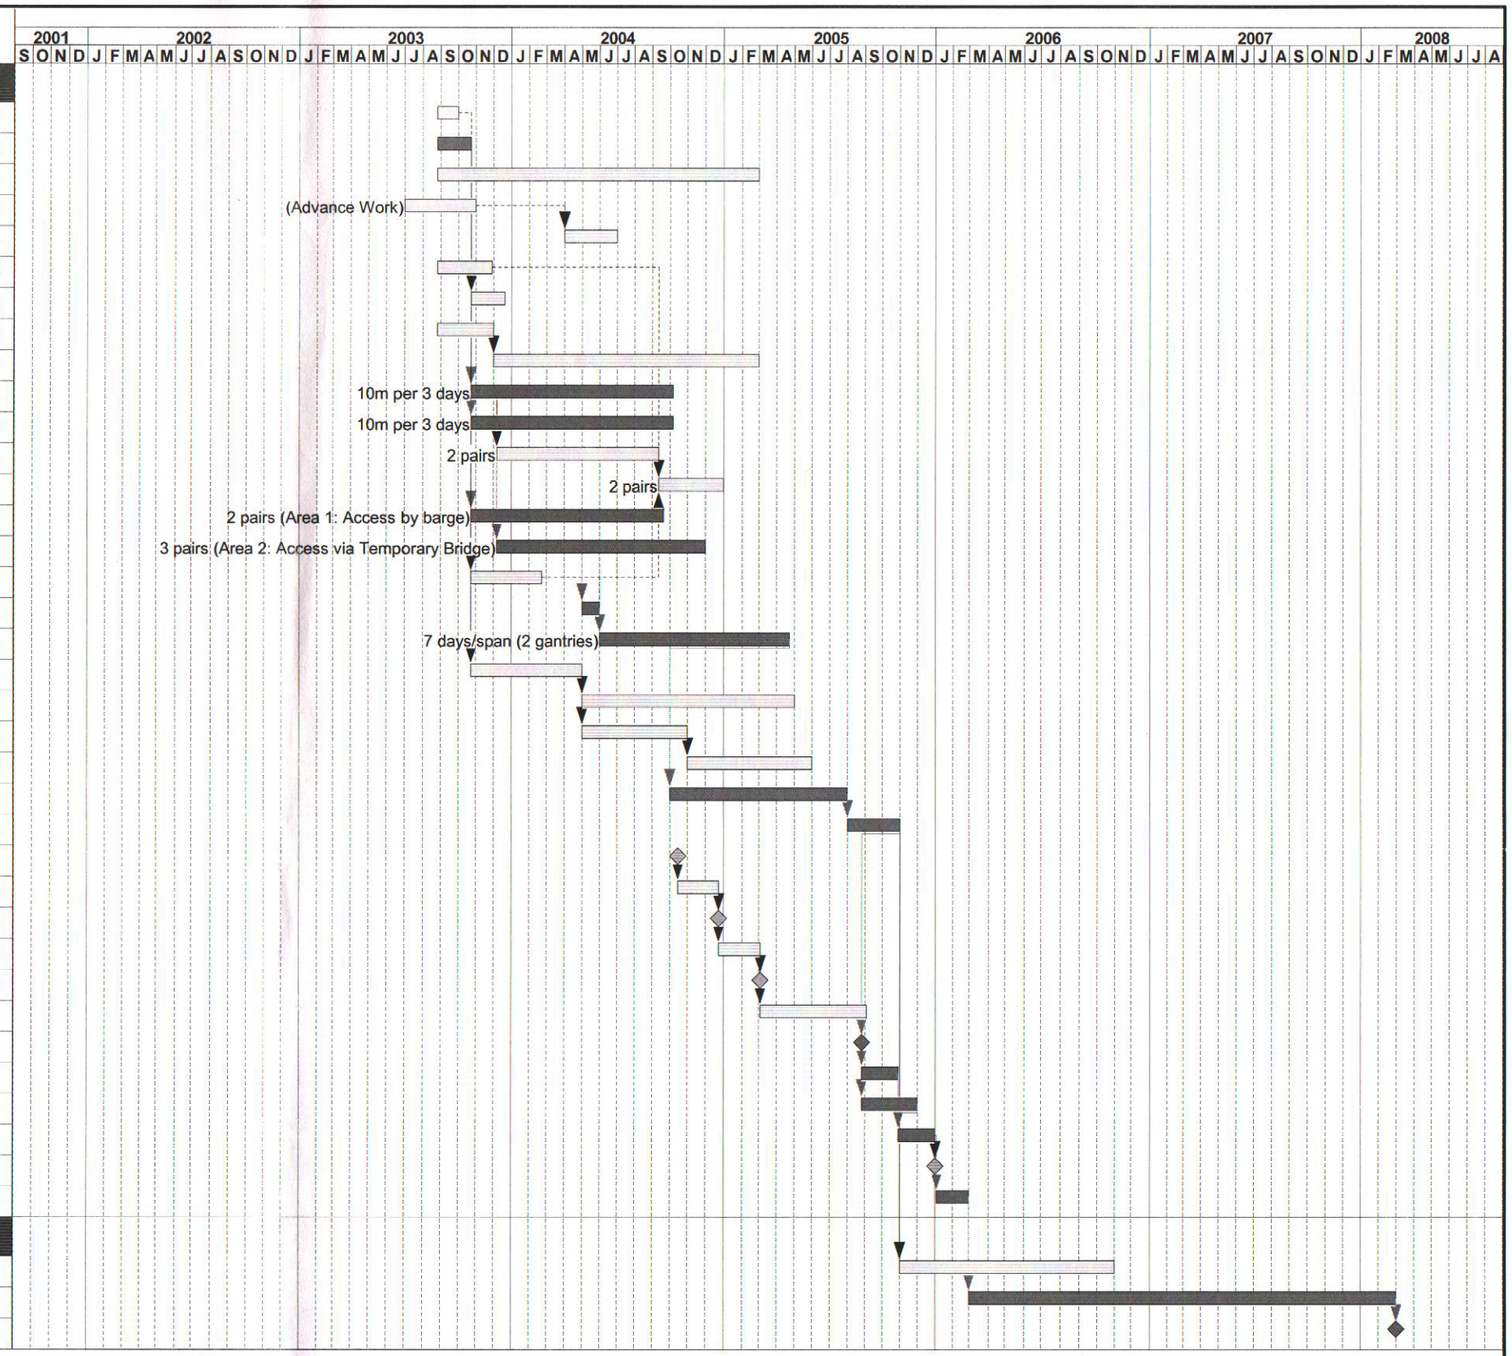

Start Date 21AUG01
Finish Date 29FEB08
Data Date 21AUG01
Run Date 02AUG02 19:03

© Primavera Systems, Inc.

Early Bar
Progress Bar
Critical Activity

Agreement No. CE51/2001
Shenzhen Western Corridor D&C

Sheet 1 of 1

Figure EM 1.3
