Act ID	Description	Orig Dur	Early Start	Early Finish
10	Site Clearance - Slip Roads A & F	25d	03APR05	27APR05
20	Site Clearance - Slip Roads B & C	25d	03APR05	27APR05
30	Site Clearance - Slip Roads D & E	90d	03APR05	01JUL05
40	Site Formation - Slip Road A & F	34d	28APR05	31MAY05
50	Site Formation - Slip Roads B & C	34d	28APR05	31MAY05
60	Site Formation - Slip Road D & E	60d	02JUL05	30AUG05
70	Construct Retaining Walls/Slope for Slip Roads	120d	01JUN05	28SEP05
80	Construct Bored Piles - Slip Road A	264d	01JUN05	19FEB06
90	Construct Bored Piles - Slip Road F	264d	01JUN05	19FEB06
100	Construct Bored Piles - Slip Road B	352d	01JUN05	18MAY06
120	Cast Pilecaps and Piers - Slip Road A	144d	17JAN06	09JUN06
130	Cast Pilecaps and Piers - Slip Road F	144d	17JAN06	09JUN06
140	Cast Pilecaps and Pier - Slip Road B	152d	17JAN06	17JUN06
150	Construct Abutment - Slip Road A	30d	31JUL05	29AUG05
160	Construct Abutment - Slip Road B	30d	31JUL05	29AUG05
170	Construct Abutment & Retaining wall- Slip Road F	30d	31JUL05	29AUG05
175	Construct Retaining wall - Slip Road F	120d	30AUG05	27DEC05
180	Construct Slip Roads D and E	210d	29SEP05	26APR06
190	Widening of Castle Peak Road	210d	28MAR06	23OCT06
200	Offsite Fabrication of Precast Concrete Segments	300d	23JUL05	18MAY06
210	Erect Segments-Slip Roads A & F	280d	19MAY06	22FEB07
220	Erect Segments - Slip Road B	220d	19MAY06	24DEC06
230	Erect Segments for side span of Slip Roads A & F	84d	19MAY06	10AUG06
240	Erect Segments for side span of Slip Road B	84d	19MAY06	10AUG06
250	Concrete Parapet & Install MJ - Slip Roads A & F	210d	08JUN06	03JAN07
260	Concrete Parapet & Install MJ - Slip Road B	280d	08JUN06	14MAR07
270	Road Pavement & Road Marking - Slip Roads A & F	85d	04DEC06	28FEB07
280	Road Pavement & Road Marking - Slip Roads B	110d	04DEC06	23MAR07
290	Landscaping Works	90d	11AUG06	08NOV06
300	Construct Bored Piles - Bridge A	75d	03APR05	16JUN05
310	Construct Abutments - Bridge A	45d	17JUN05	31JUL05
320	Offsite Prefabrication of Steel Truss-Bridge A	120d	03APR05	31JUL05
330	Deck Erection & Casting - Bridge A	45d	01AUG05	14SEP05
340	Road Pavement - Bridge A	14d	15SEP05	28SEP05

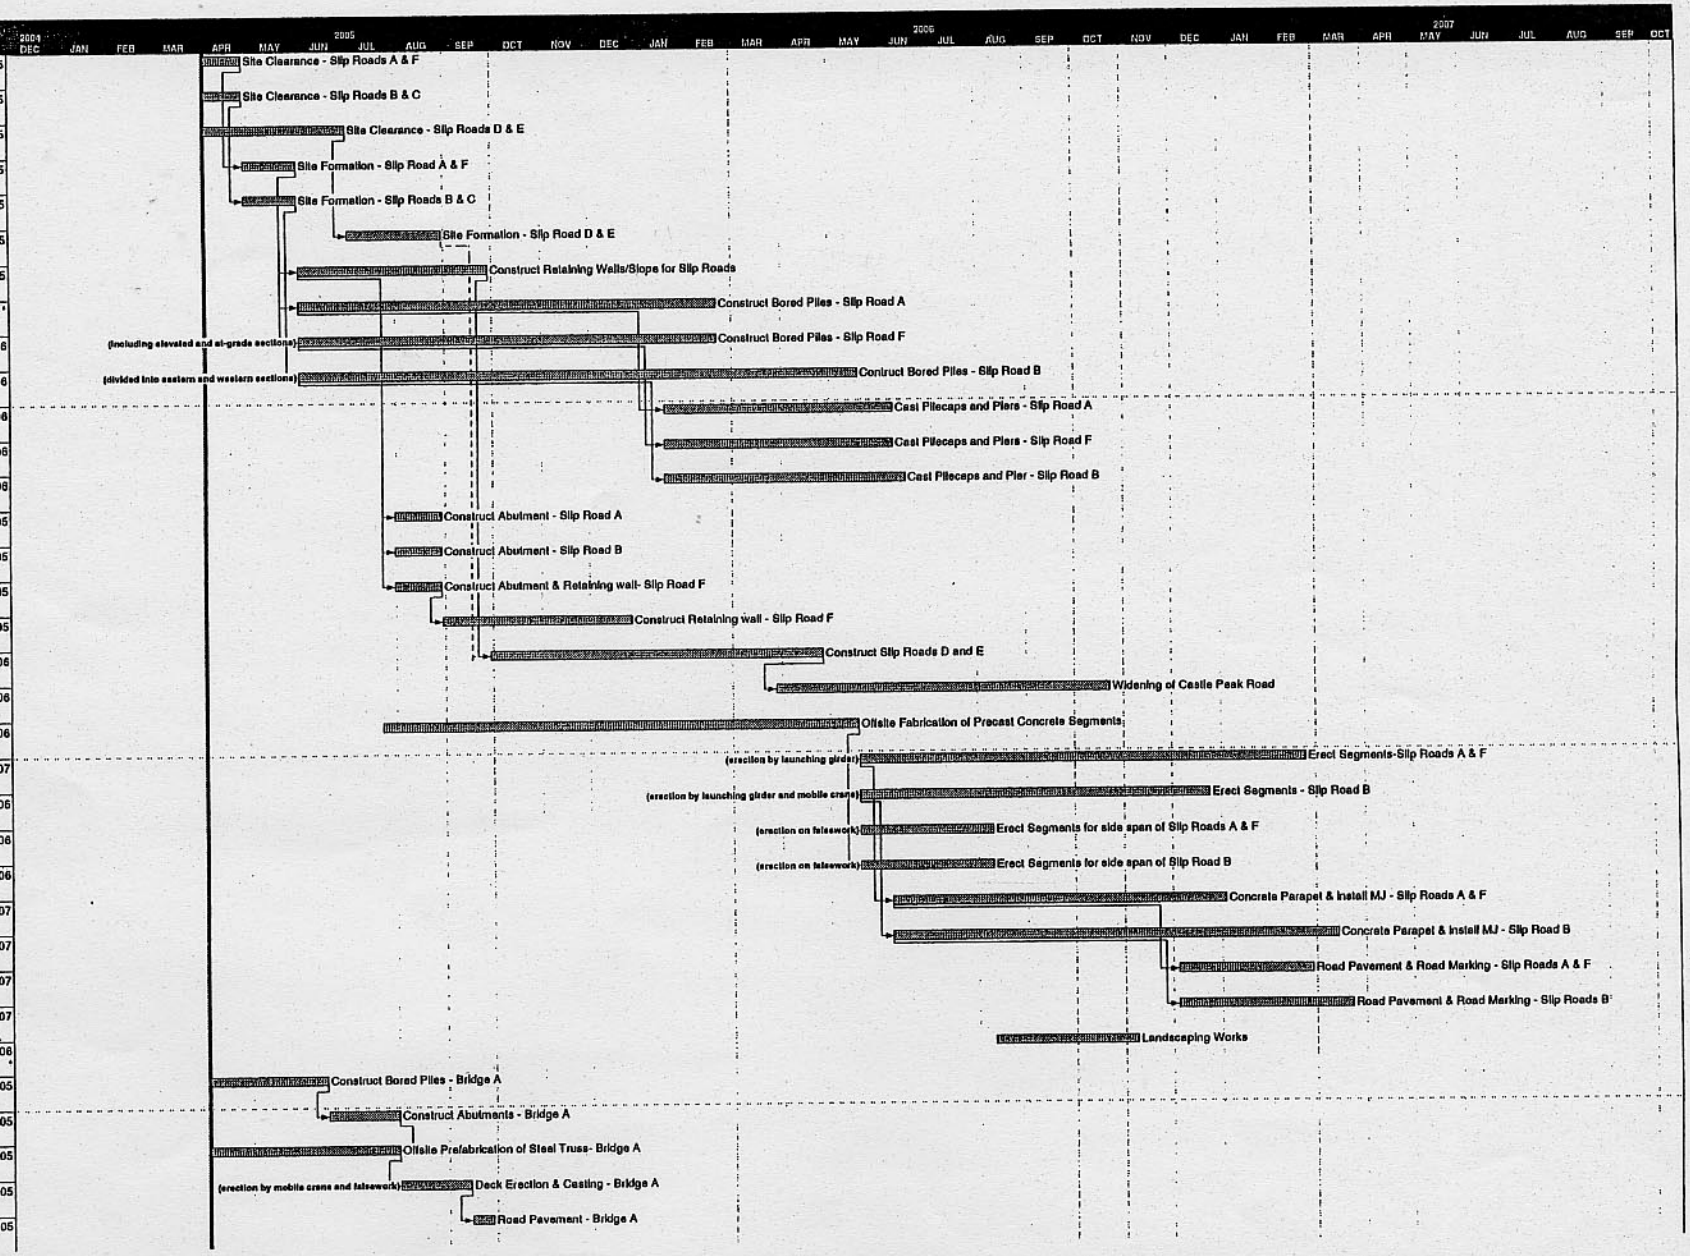

Maunsell
ENVIRONMENTAL MANAGEMENT CONSULTANTS LTD.
茂盛環境管理顧問有限公司

AGREEMENT NO. CE 38/2002 (HY)
IMPROVEMENT TO SAN TIN INTERCHANGE - INVESTIGATION - EIA STUDY

PRELIMINARY CONSTRUCTION PROGRAMME

SCALE 比例	N.T.S.
DATE 日期	DEC 03
JOB No. 項目編號	A07502
DRAWING No. 圖號	1.2
