Appendix 2.5
Construction Programme

Act ID	Description	Orig Dur	Early Start	Early Finish
1. CAUSEWAY BAY RECLAMATION				
		2233d	02JAN09	03MAR16
1.1 Temporary Relocation CBTS				
		2229d	02JAN09	27FEB16
Temporary Breakwater				
		149d	02JAN09	24JUN09
1011010	Mobilisation	26d	02JAN09	31JAN09
1011030	Dredging Temporary Breakwater	112d	02FEB09	11JUN09
1011040	RockFilling	58d	06APR09	11JUN09
1011050	Amour placing	11d	12JUN09	24JUN09
1011060	Bored Pile Walls	60d	02FEB09	11APR09
Relocation Mooring to Temp CBTS				
		52d	25JUN09	24AUG09
1013000	Install temporary moorings	26d	25JUN09	24JUL09
1013010	Moving moorings to Temp CBTS	26d	25JUL09	24AUG09
Relocation Mooring back to CBTS				
		86d	18NOV15	27FEB16
1014040	Install new moorings in CBTS	26d	18NOV15	17DEC15
1014070	Relocate moorings to CBTS	0		17DEC15
1014080	Removal of temporary breakwater and piles	60d	18DEC15	27FEB16
1.2 CBTS Temporary Reclamation Stage 1				
		840d	25AUG09	03MAY12
Dredging, temp seawall & Filling TCBR1				
		206d	25AUG09	23APR10
1021009	Dredging TCBR1E	32d	25AUG09	30SEP09
1021010	Rockfill to TCBR1E temporary seawall	29d	01OCT09	03NOV09
1021020	Temp Seawall construction TCBR1E	54d	04NOV09	07JAN10
1021030	Filling behind seawall TCBR1E	29d	08JAN10	10FEB10
1031000	Dredging TCBR1W	40d	01OCT09	16NOV09
1031010	Rockfill to TCBR1W temp seawall	34d	17NOV09	26DEC09
1031020	Temp seawall construction TCBR1W	62d	28DEC09	10MAR10
1031030	Filling behind temp seawall TCBR1W	38d	11MAR10	23APR10
CWB Tunnel (TCBR1)				
		696d	11FEB10	03MAY12
1022010	Diaphragm walls (TCBR1E)	95d	11FEB10	01JUN10
1022020	Excavation (TCBR1E) (to filling TCBR2)	116d	28APR10	08SEP10
1022030	Slab construction (TCBR1E)	52d	01SEP10	30OCT10
1022040	Backfill up to -4.0 mPD(TCBR1E)	18d	01NOV10	20NOV10
1022050	Removal Tempporary Seawall (TCBR1E)	30d	22NOV10	27DEC10
1032000	Diaphragm walls (TCBR1W)	148d	24APR10	12OCT10
1032020	Excavation (TCBR1W)	160d	04AUG10	08FEB11
1032030	Slab construction (TCB1W)	84d	24JAN11	30APR11
1032040	Backfill up to -4.0 mPD(TCB1W)	106d	28NOV11	29MAR12
1032050	Removal Temporary Seawall (TCB1W)	30d	30MAR12	03MAY12
CWB Tunnel (CHT)				
		250d	09FEB11	26NOV11
1033010	Rock Excavation (CHT)	180d	09FEB11	06SEP11
1033020	Slab Construction (CHT)	70d	07SEP11	26NOV11
1.3 CBTS Temporary Reclamation Stage 2				
		791d	17NOV09	30MAY12
Dredging, Temp Seawall & Filling (TCBR2)				
		173d	17NOV09	08JUN10
1041009	Dredging (TCBR2)	39d	17NOV09	02JAN10
1041010	Rockfill to temporary seawall (TCBR2)	34d	04JAN10	11FEB10
1041020	Seawall construction TCBR2	62d	12FEB10	24APR10
1041030	Filling behind seawall TCBR2 (from TCBR1E)	36d	28APR10	08JUN10

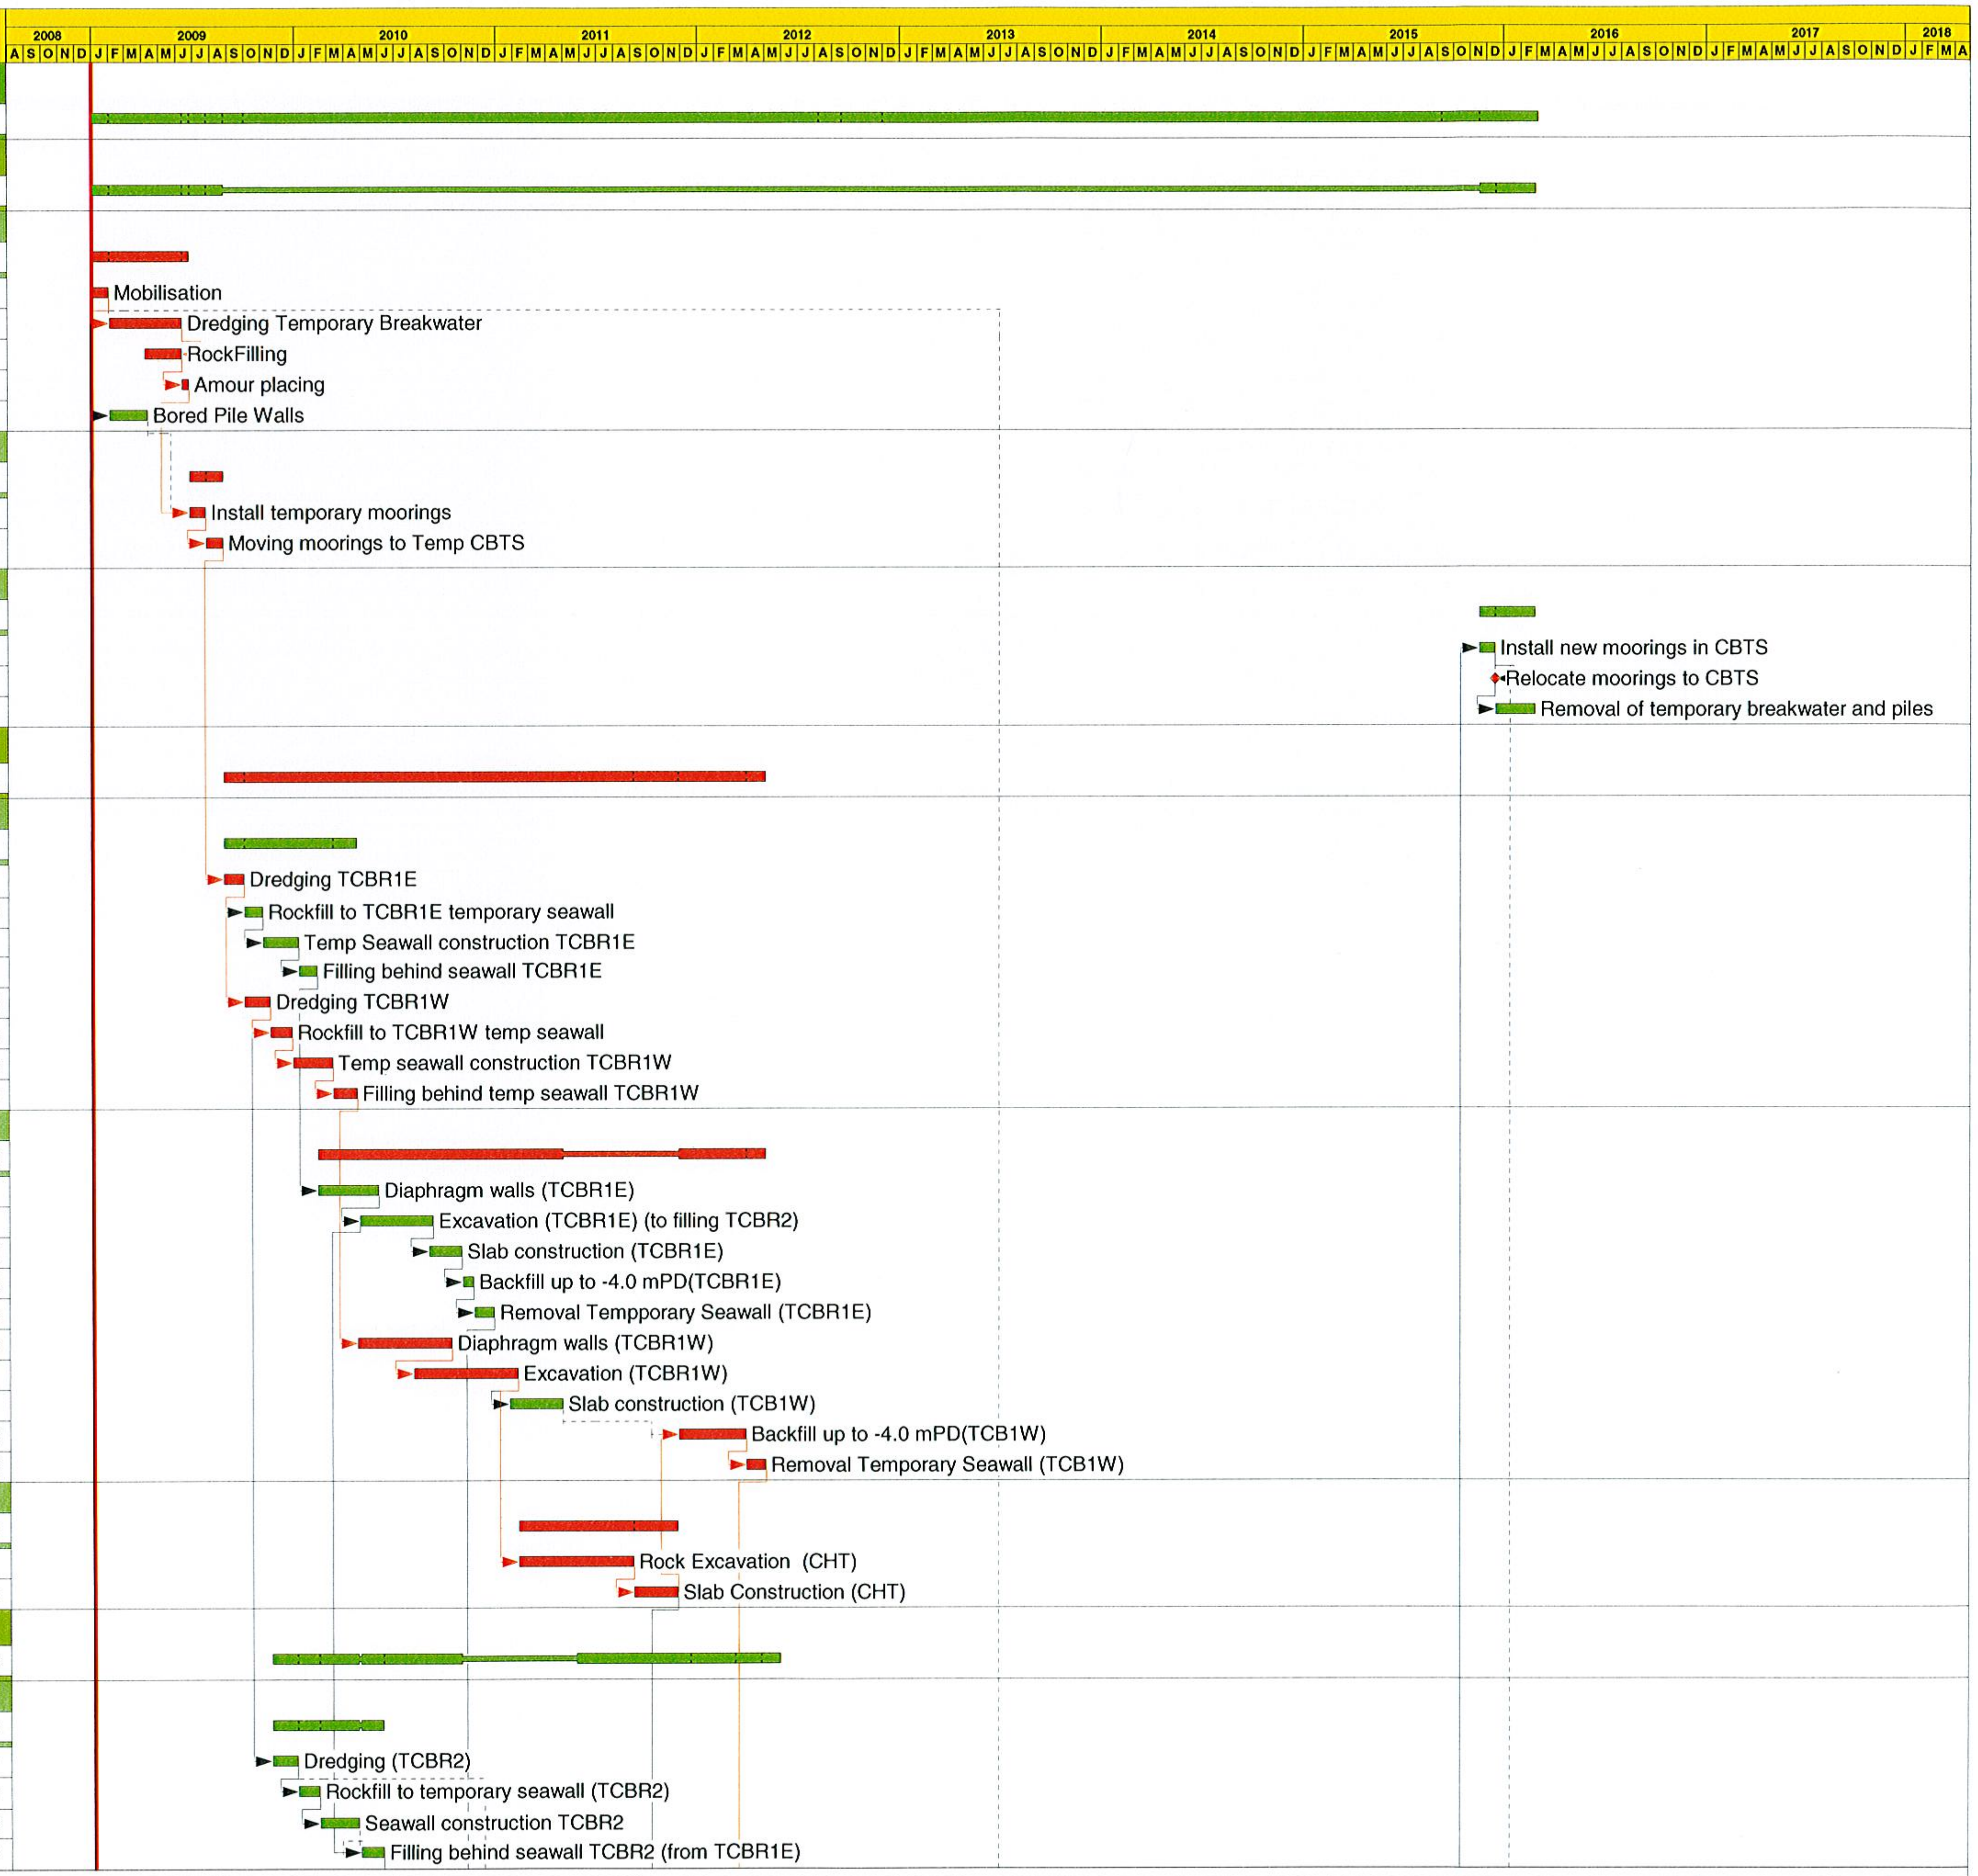

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	1A

Act ID	Description	Orig Dur	Early Start	Early Finish
	CWB Tunnel (TCBR2)			
		618d	09JUN10	30MAY12
1042000	Diaphragm walls TCBR2	124d	09JUN10	29OCT10
1042020	Excavation TCBR2 (to filling TCBR3)	179d	25MAY11	19DEC11
1042030	Slab construction TCBR2	70d	20DEC11	09MAR12
1042040	Backfill up to -4.0 mPDTCBR2	40d	10MAR12	25APR12
1042050	Removal Temporary Seawall TCBR2	30d	26APR12	30MAY12
	1.4 CBTS Temporary Reclamation Stage 3			
		994d	28JAN11	05APR14
	Dredging, Temp Seawall & Filling (TCBR3)			
		179d	28JAN11	24AUG11
1051000	Dredging TCBR3	41d	28JAN11	16MAR11
1051060	Rockfill temporary seawall TCBR3	35d	17MAR11	26APR11
1051070	Seawall construction TCBR3	64d	27APR11	09JUL11
1051080	Filling behind seawall TCBRE3 (from TCBR2 & CHT)	39d	11JUL11	24AUG11
	CWB Tunnel (TCBR3)			
		815d	25AUG11	05APR14
1052000	Diaphragm walls TCBR3	134d	25AUG11	27JAN12
1052020	Excavation TCBR3 (to filling TCBR4)	224d	16JAN13	03OCT13
1052030	Slab construction TCBR3	78d	18SEP13	17DEC13
1052040	Backfill up to -4.0 mPD TCBR3	62d	18DEC13	01MAR14
1052050	Removal Temporary Seawall TCBR3	30d	03MAR14	05APR14
	1.5 CBTS Temporary Reclamation Stage 4			
		1102d	04MAY12	17NOV15
	Dredging, Temp Seawall & Filling (TCBR4)			
		280d	04MAY12	28MAR13
1061000	Dredging TCBR4	82d	04MAY12	07AUG12
1061060	Rockfill temporary seawall TCBR4	35d	08AUG12	17SEP12
1061070	Seawall construction TCBR4	64d	18SEP12	30NOV12
1061080	Filling behind seawall TCBR4 (from TCBR3)	99d	01DEC12	28MAR13
	CWB Tunnel (TCBR4)			
		822d	29MAR13	17NOV15
1062000	Diaphragm walls (TCBR4)	350d	29MAR13	13MAY14
1062020	Excavation (TCBR4)	350d	19OCT13	03DEC14
1062030	Slab construction (TCBR4)	208d	05AUG14	06APR15
1062040	Backfill up to -4.0 mPD(TCBR4)	233d	09DEC14	08SEP15
1062050	Removal Temporary Seawall (TCBR4)	60d	09SEP15	17NOV15
	1.6 Temp Diversion of Cooling Water System			
		1626d	27OCT10	16JAN16
1063010	Construct Temporary Intake pipeline	26d	27OCT10	25NOV10
1063020	Temp Outfall pipeline	26d	26NOV10	27DEC10
1063030	Commissioning	26d	28DEC10	27JAN11
1063040	Reinstate Pump House	20d	18NOV15	10DEC15
1063050	Commissioning original pump house	30d	11DEC15	16JAN16
	1.7 Promenade along CBTS			
		90d	18NOV15	03MAR16
1110000	Interim paving & landscaping, boardwalk	90d	18NOV15	03MAR16
	1.9 Slip Road 8 & Victoria Park Reprovisioning			
		506d	02AUG13	19MAR15
	Victoria Park Road Traffic Diversion			
		111d	06FEB14	14JUN14
1091000	TTA for Victoria Park Rd E/B	14d	06FEB14	21FEB14
1091010	TTA for Victoria Park Rd W/B	14d	30MAY14	14JUN14
	Slip Road 8 Tunnel			
		263d	15NOV13	19SEP14
1092000	SR8 Tunnel under VP Rd E/B	83d	22FEB14	29MAY14

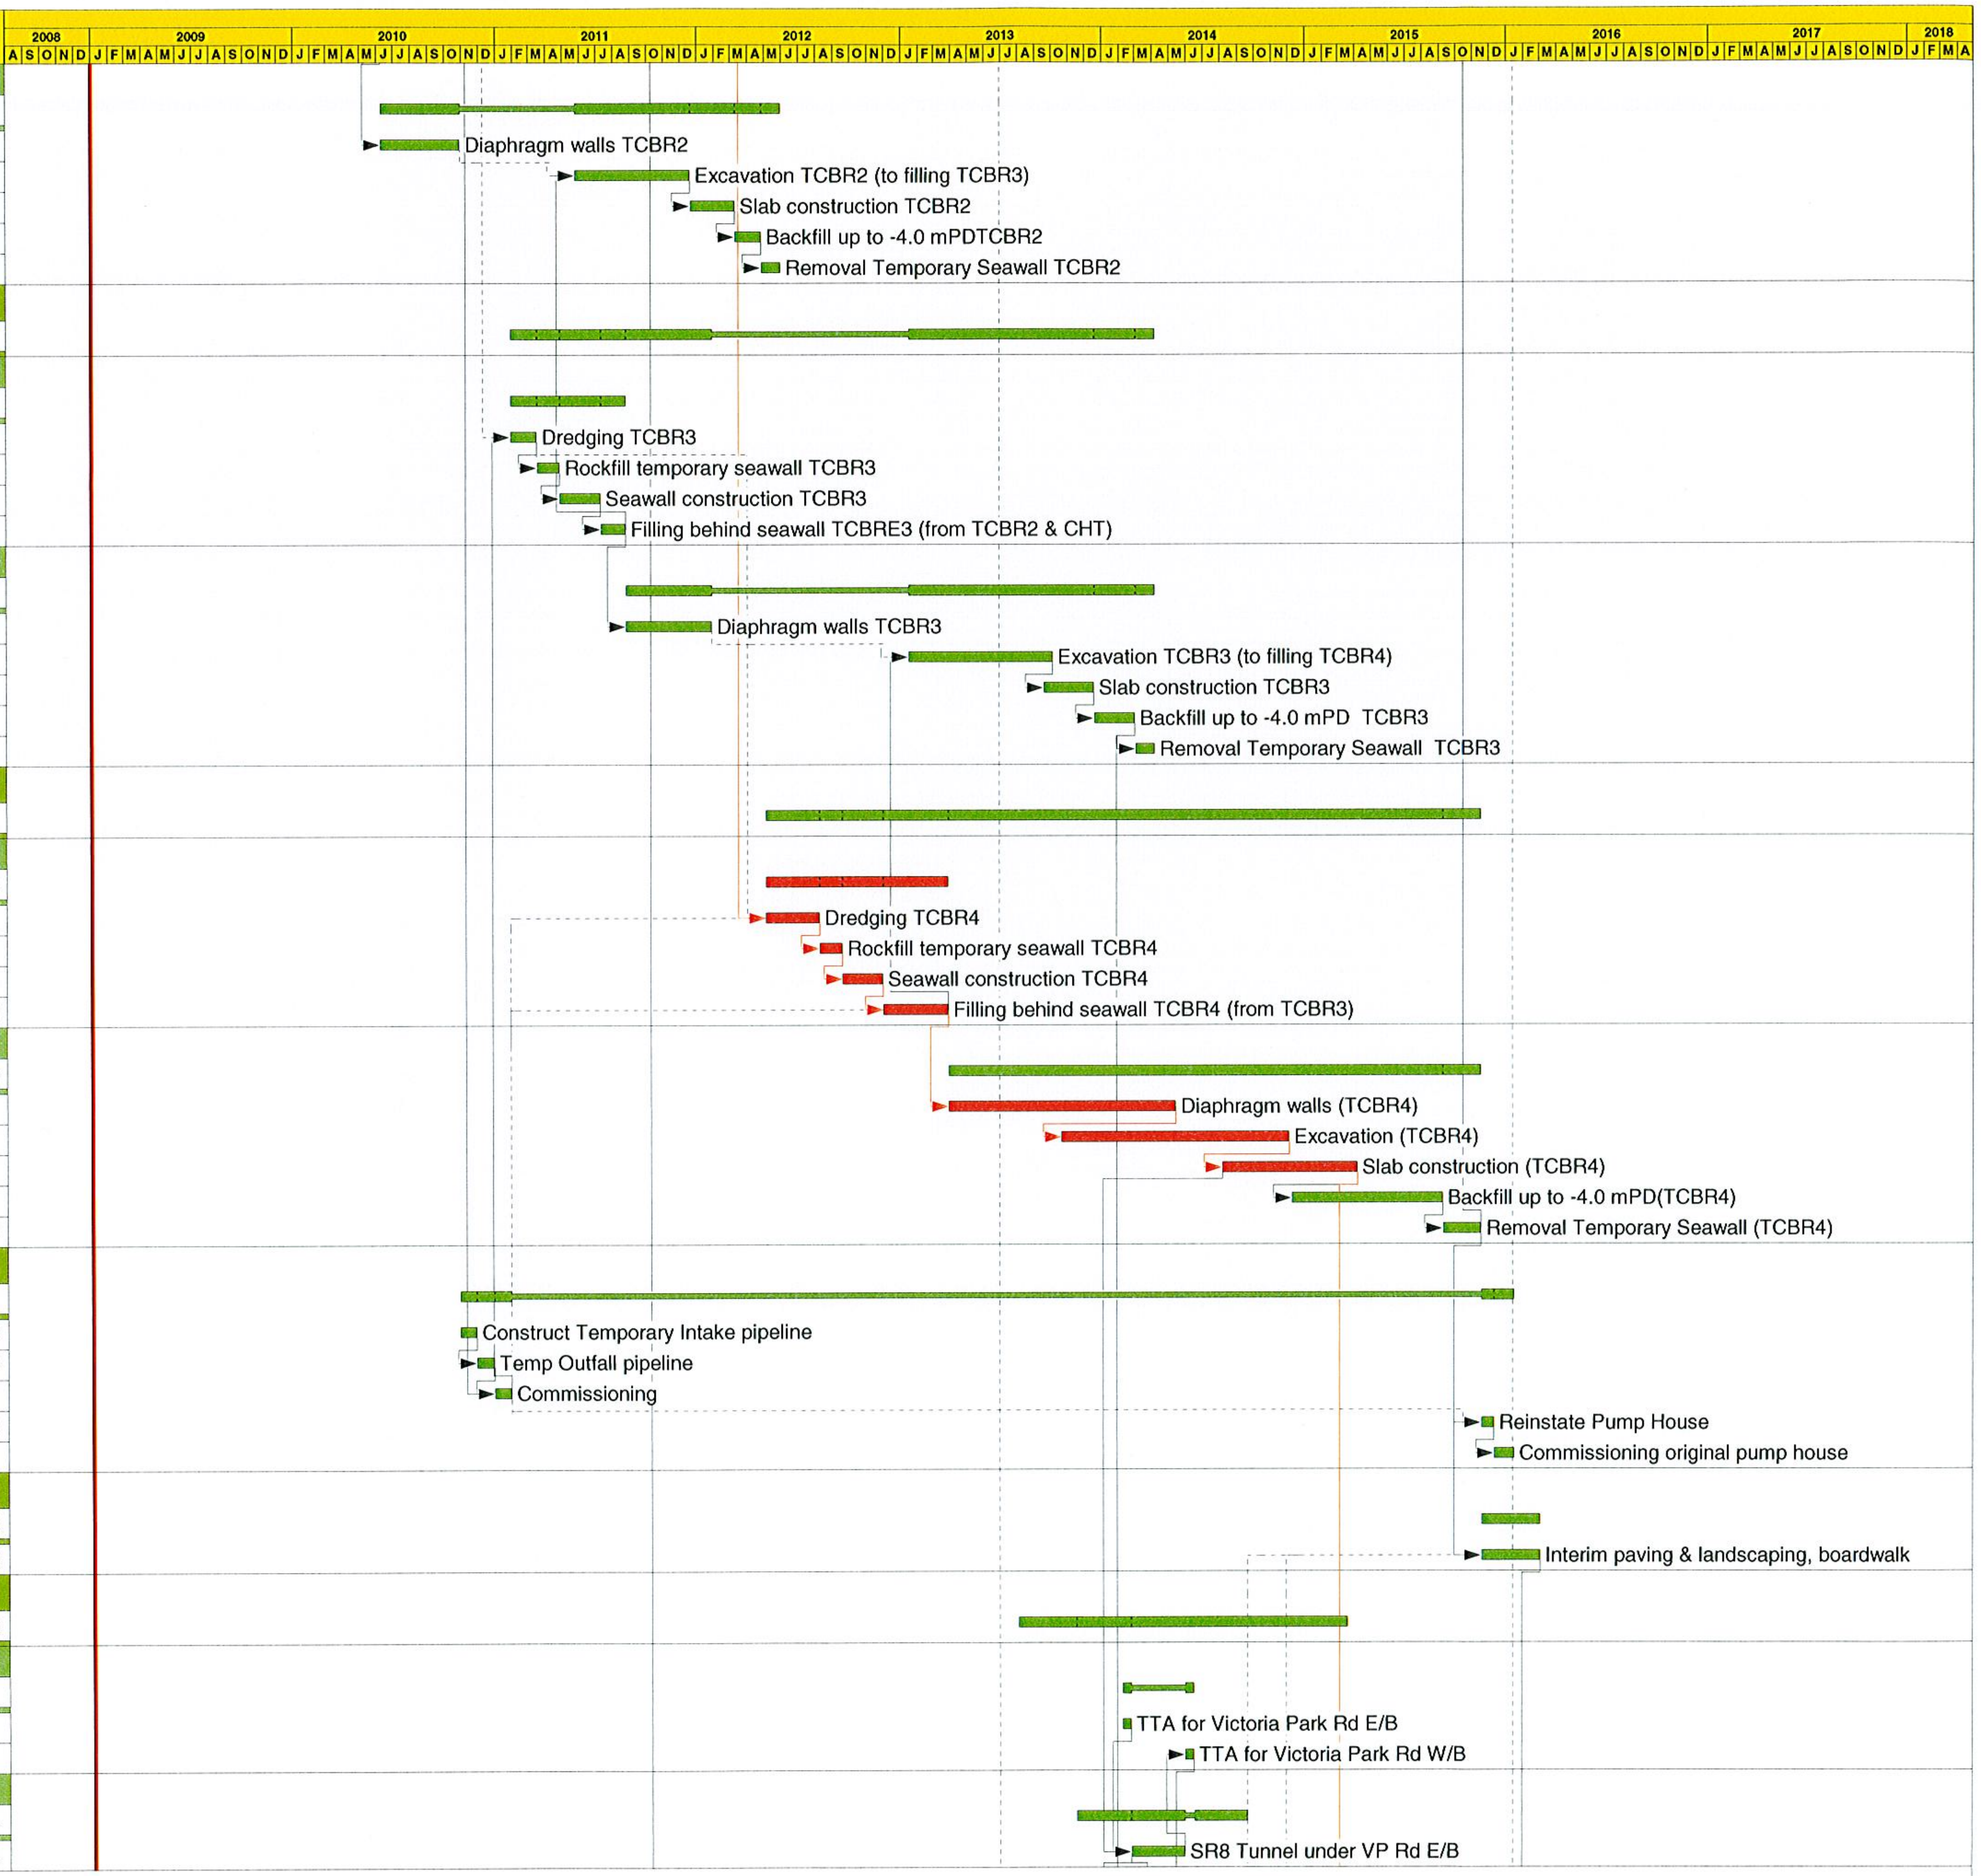

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	2A

Act ID	Description	Orig Dur	Early Start	Early Finish
1092010	SR8 Tunnel under VP Rd W/B	83d	16JUN14	19SEP14
1092020	SR8 Tunnel in Victoria Park	83d	15NOV13	21FEB14
Transplant Trees in Victoria Park				
		90d	02AUG13	14NOV13
1093000	Transplant Victoria Park Tree	90d	02AUG13	14NOV13
At-grade road				
		240d	22FEB14	28NOV14
1094000	At-grade Road work in Victoria Park Road	90d	22FEB14	06JUN14
1094010	Reinstate Victoria Park Road W/B	30d	20SEP14	24OCT14
1094020	Reinstate Victoria Park Road E/B	30d	25OCT14	28NOV14
Landscape Deck				
		273d	22FEB14	08JAN15
1095000	Substructure for Landscape Deck	93d	22FEB14	10JUN14
1095010	Superstructure work for Landscape Deck	150d	11JUN14	02DEC14
1095020	Soft and hard landscape work on deck	30d	03DEC14	08JAN15
Reinstate Landscape work in VP				
		90d	03DEC14	19MAR15
1096000	Reinstate soft landscape work in Victoria Park	90d	03DEC14	19MAR15
1.10 Handover / Completion Dates				
		624d	01MAR14	03MAR16
1100000	Handover Stage 1 Tunnel (E) to HyD for CWB	0		01MAR14
1100010	Handover Stage 2 Tunnel (W) to HyD for CWB	0		06APR15
1100030	Completion of CBR construction	0		03MAR16
2. Ex-PCWA Temporary Reclamation				
		1970d	02FEB09	29MAY15
2.1 Temporary Reclamation PCWA Stage 1				
		1016d	02FEB09	04MAY12
Dredging, Filling and Seawall (PCWAE)				
		70d	02FEB09	23APR09
211000	Dredging (PCWAE)	16d	02FEB09	19FEB09
211010	Rockfill for Temp. seawall (PCWAE)	12d	20FEB09	05MAR09
211020	Temp seawall (PCWAE)	22d	06MAR09	31MAR09
211030	Filling behind temp seawall (PCWAE)	20d	01APR09	23APR09
CWB Tunnel (PCWAE)				
		946d	24APR09	04MAY12
212000	Diaphragm walls (PCWAE)	135d	24APR09	28SEP09
212010	Excavation (PCWAE)	221d	29SEP09	15JUN10
212020	Slab construction (PCWAE)	64d	16JUN10	27AUG10
212030	Backfill up to -4.0 mPD(PCWAE)	77d	28NOV11	24FEB12
212040	Removal Temporary Seawall & PCWAE	60d	25FEB12	04MAY12
2.2. Temporary Reclamation PCWA Stage 2				
		1002d	10MAR12	29MAY15
Dredging, filling and Seawall (PCWAW)				
		71d	10MAR12	31MAY12
221000	Dredging (PCWAW)	20d	10MAR12	02APR12
221010	Rockfill for Temp. seawall (PCWAW)	10d	03APR12	13APR12
221020	Temp seawall (PCWAW)	18d	14APR12	04MAY12
221030	Filling behind temp seawall (PCWAW)	23d	05MAY12	31MAY12
CWB Tunnel (PCWAW)				
		931d	01JUN12	29MAY15
222000	Diaphragm walls (PCWAW)	187d	01JUN12	07JAN13
222010	Excavation (PCWAW)	257d	08JAN13	02NOV13
222020	Slab construction (PCWAW)	75d	04NOV13	31JAN14
222030	Backfill up to -4.0 mPD(PCWAW)	89d	01FEB14	15MAY14
222040	Remove temporary seawall & PCWAW	60d	21MAR15	29MAY15

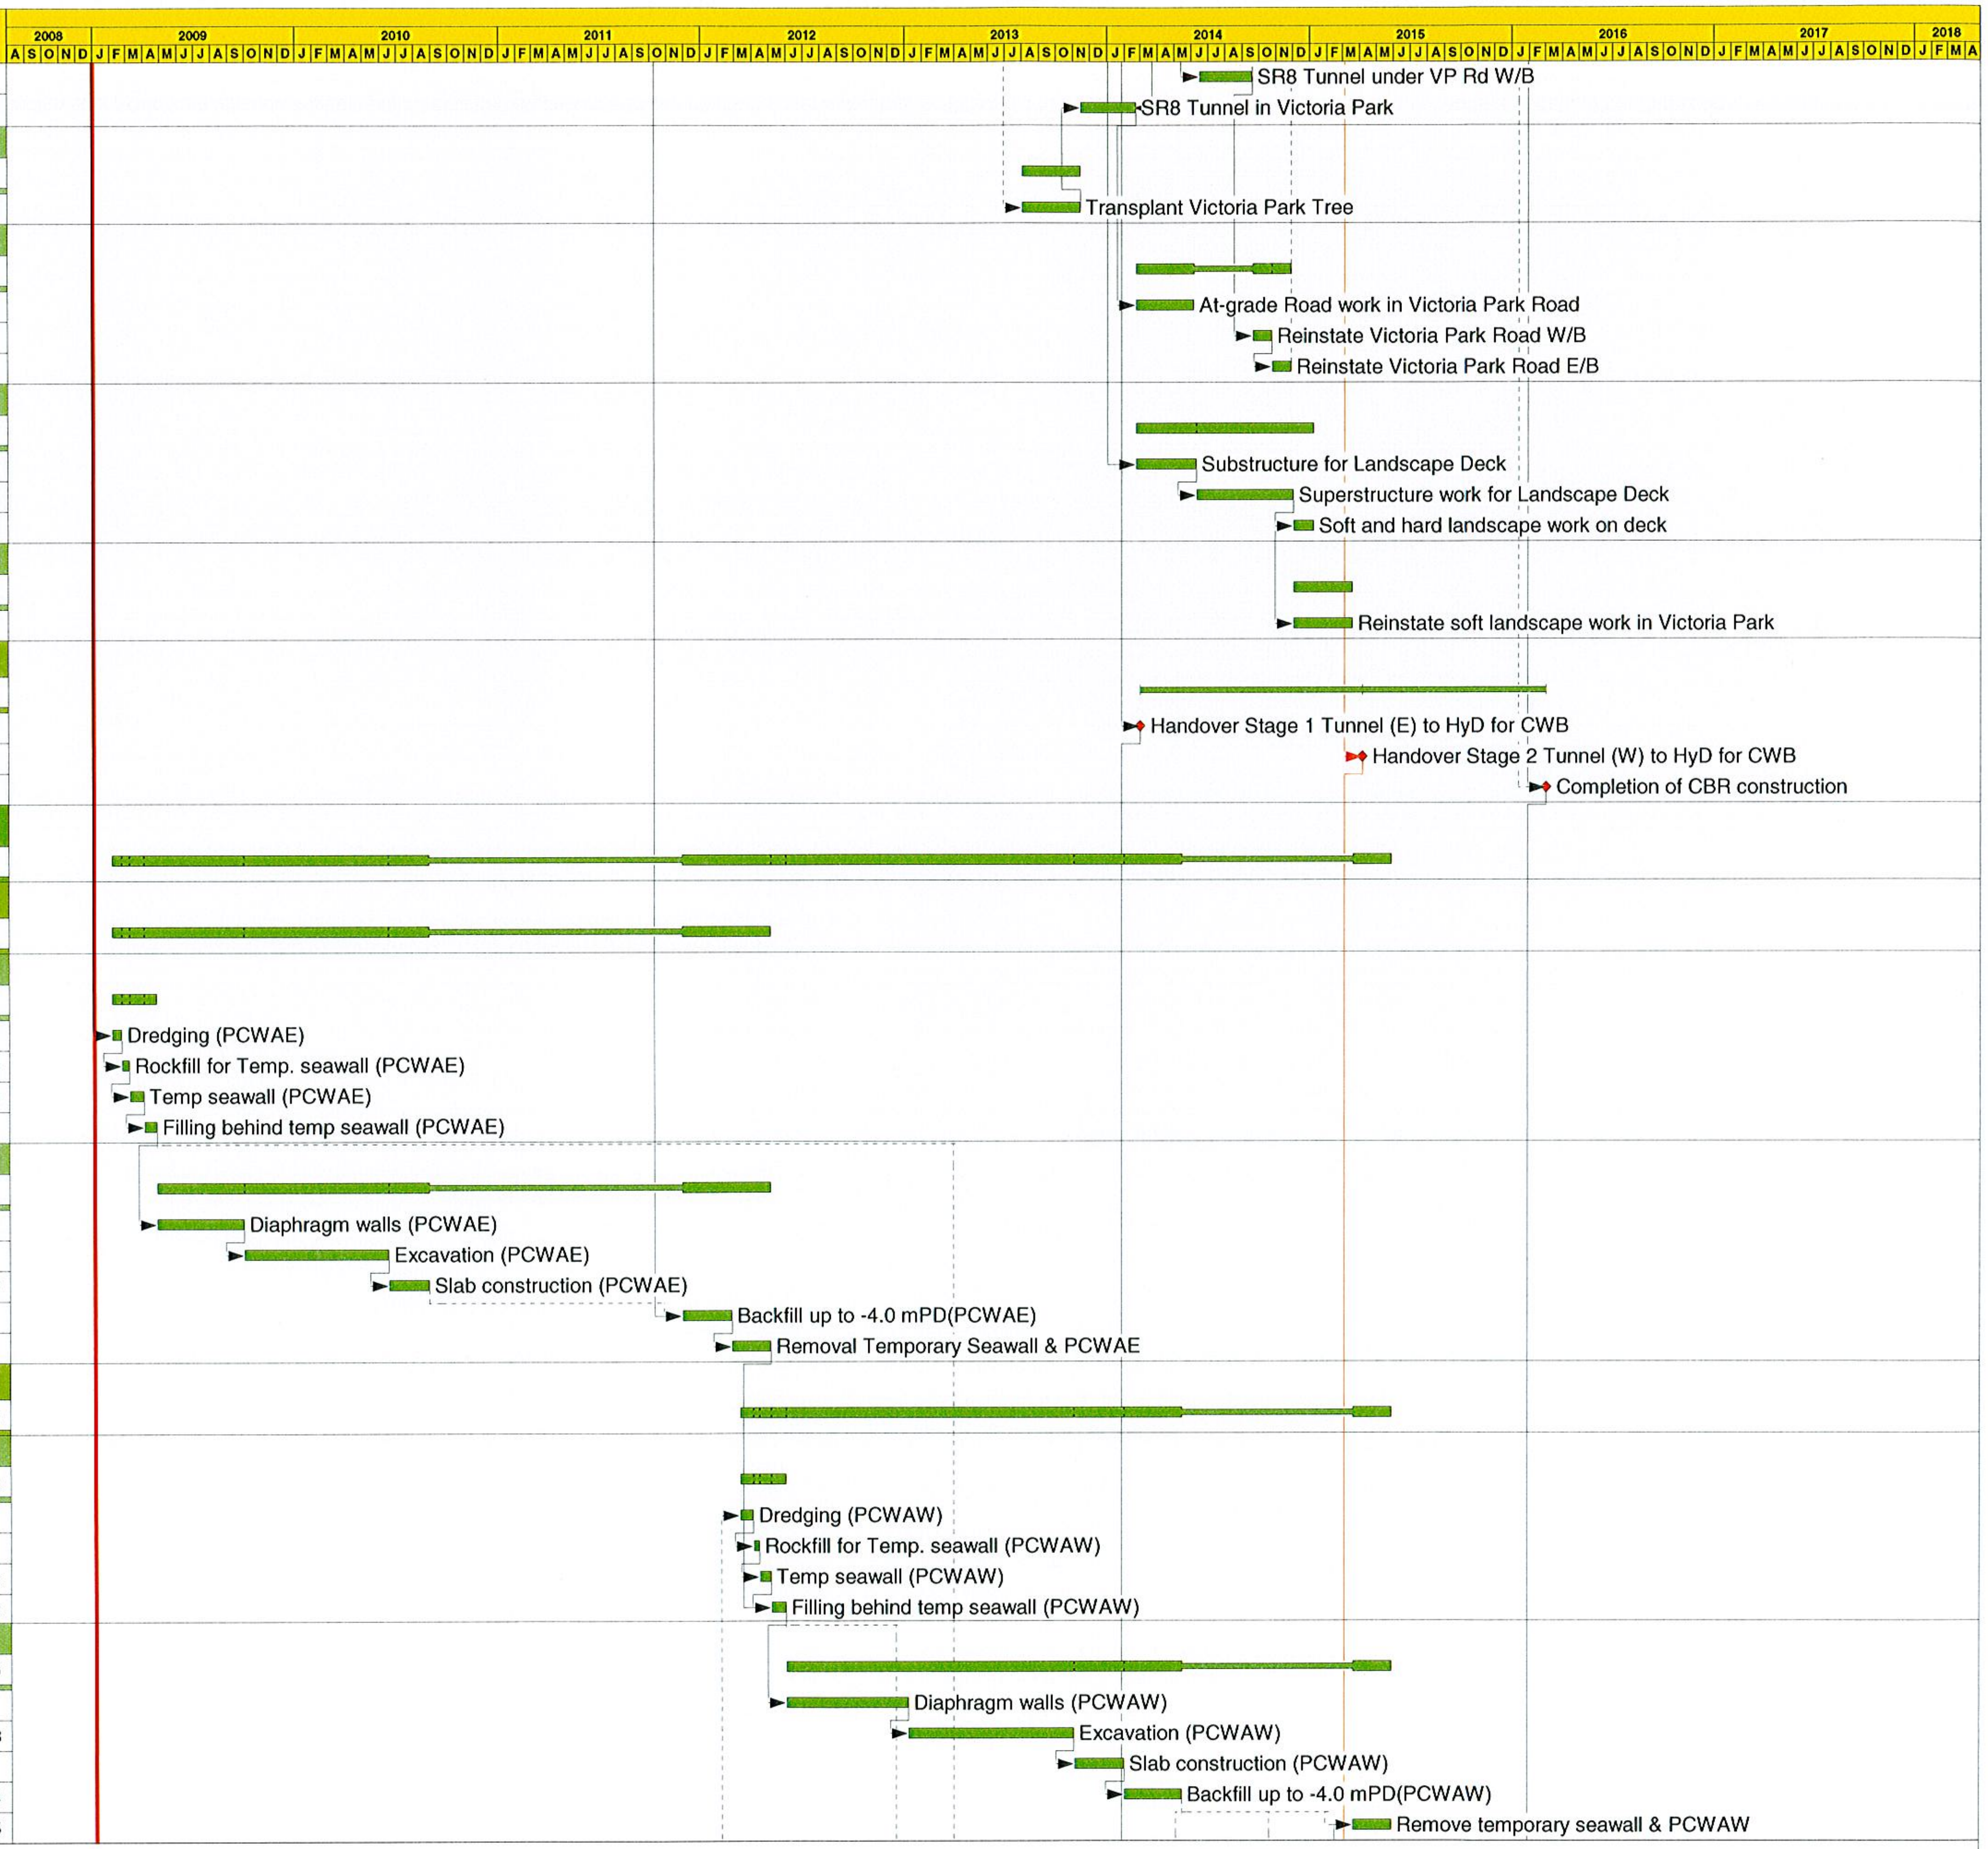

Act ID	Description	Orig Dur	Early Start	Early Finish
3	**WAN CHAI RECLAMATION**			
		2091d	02JAN09	17SEP15
3.1	**Wan Chai Reclamation Stage 1**			
		671d	02JAN09	26FEB11
	Dredging, Seawalls & Filling			
		342d	02JAN09	06FEB10
311000	Mobilisation	26d	02JAN09	31JAN09
311020	Dredging (WCR1)	29d	02FEB09	06MAR09
311030	Rockfill for seawall foundations (WCR1)	41d	27MAR09	13MAY09
311040	Seawall construction (WCR1)	46d	18JUN09	10AUG09
311045	Rockfill for temp seawall (WCR1)	17d	07MAR09	26MAR09
311046	Temp seawall construction (WCR1)	30d	14MAY09	17JUN09
311050	Filling behind seawall (WCR1)	29d	03SEP09	06OCT09
311060	Surcharge & consolidation (WCR1)	104d	07OCT09	06FEB10
	Drainage Culverts			
		645d	02FEB09	26FEB11
312000	Culvert N widening	25d	02FEB09	02MAR09
312020	Culvert N1 (2 cell box culvert)	102d	29OCT10	26FEB11
	Cooling Water Systems			
		621d	02FEB09	29JAN11
313000	Precast caisson units	104d	02FEB09	02JUN09
313010	Place caisson units	24d	14JUL09	10AUG09
313015	M&E works	78d	11AUG09	09NOV09
313020	Intake pipelines	26d	29OCT10	27NOV10
313030	Outfall pipelines	26d	29OCT10	27NOV10
313040	Commissioning	52d	29NOV10	29JAN11
	CWB Tunnel (WCR1)			
		304d	08FEB10	28JAN11
314000	Diaphragm walls (WCR1)	124d	08FEB10	01JUL10
314010	Excavation (WCR1)	179d	08MAR10	30SEP10
314020	Slab construction (WCR1)	65d	14AUG10	28OCT10
314030	Backfill (WCR1)	77d	29OCT10	28JAN11
3.2	**Wan Chai Reclamation Stage 2**			
		711d	31JAN11	10MAY13
	Dredging, Seawalls & Filling			
		166d	31JAN11	11AUG11
321000	Dredging WCR2	15d	31JAN11	16FEB11
321010	Temp Seawall constuction WCR2	23d	17FEB11	15MAR11
321030	Filling behind seawall WCR2	24d	16MAR11	12APR11
321040	Surcharge & consolidation WCR2	104d	13APR11	11AUG11
	CWB Tunnel			
		389d	12AUG11	07NOV12
323000	Diaphragm walls WCR2	105d	12AUG11	12DEC11
323010	Excavation WRC2	184d	15NOV11	15JUN12
323020	Slab construction WRC2	73d	19MAY12	11AUG12
323030	Backfill WRC2	75d	13AUG12	07NOV12
	Promenade			
		156d	08NOV12	10MAY13
324000	Interim paving & landscaping (+ WCR1)	104d	08NOV12	11MAR13
324010	Complete paving & landscaping	52d	12MAR13	10MAY13
3.3	**Wan Chai Reclamation Stage 3**			
		1226d	13APR11	19MAR15
	Dredging, Seawalls & Filling			
		585d	13APR11	25FEB13
331000	Dredging WCR3	32d	13APR11	19MAY11
331010	Seawall foundations WCR3	25d	20MAY11	17JUN11

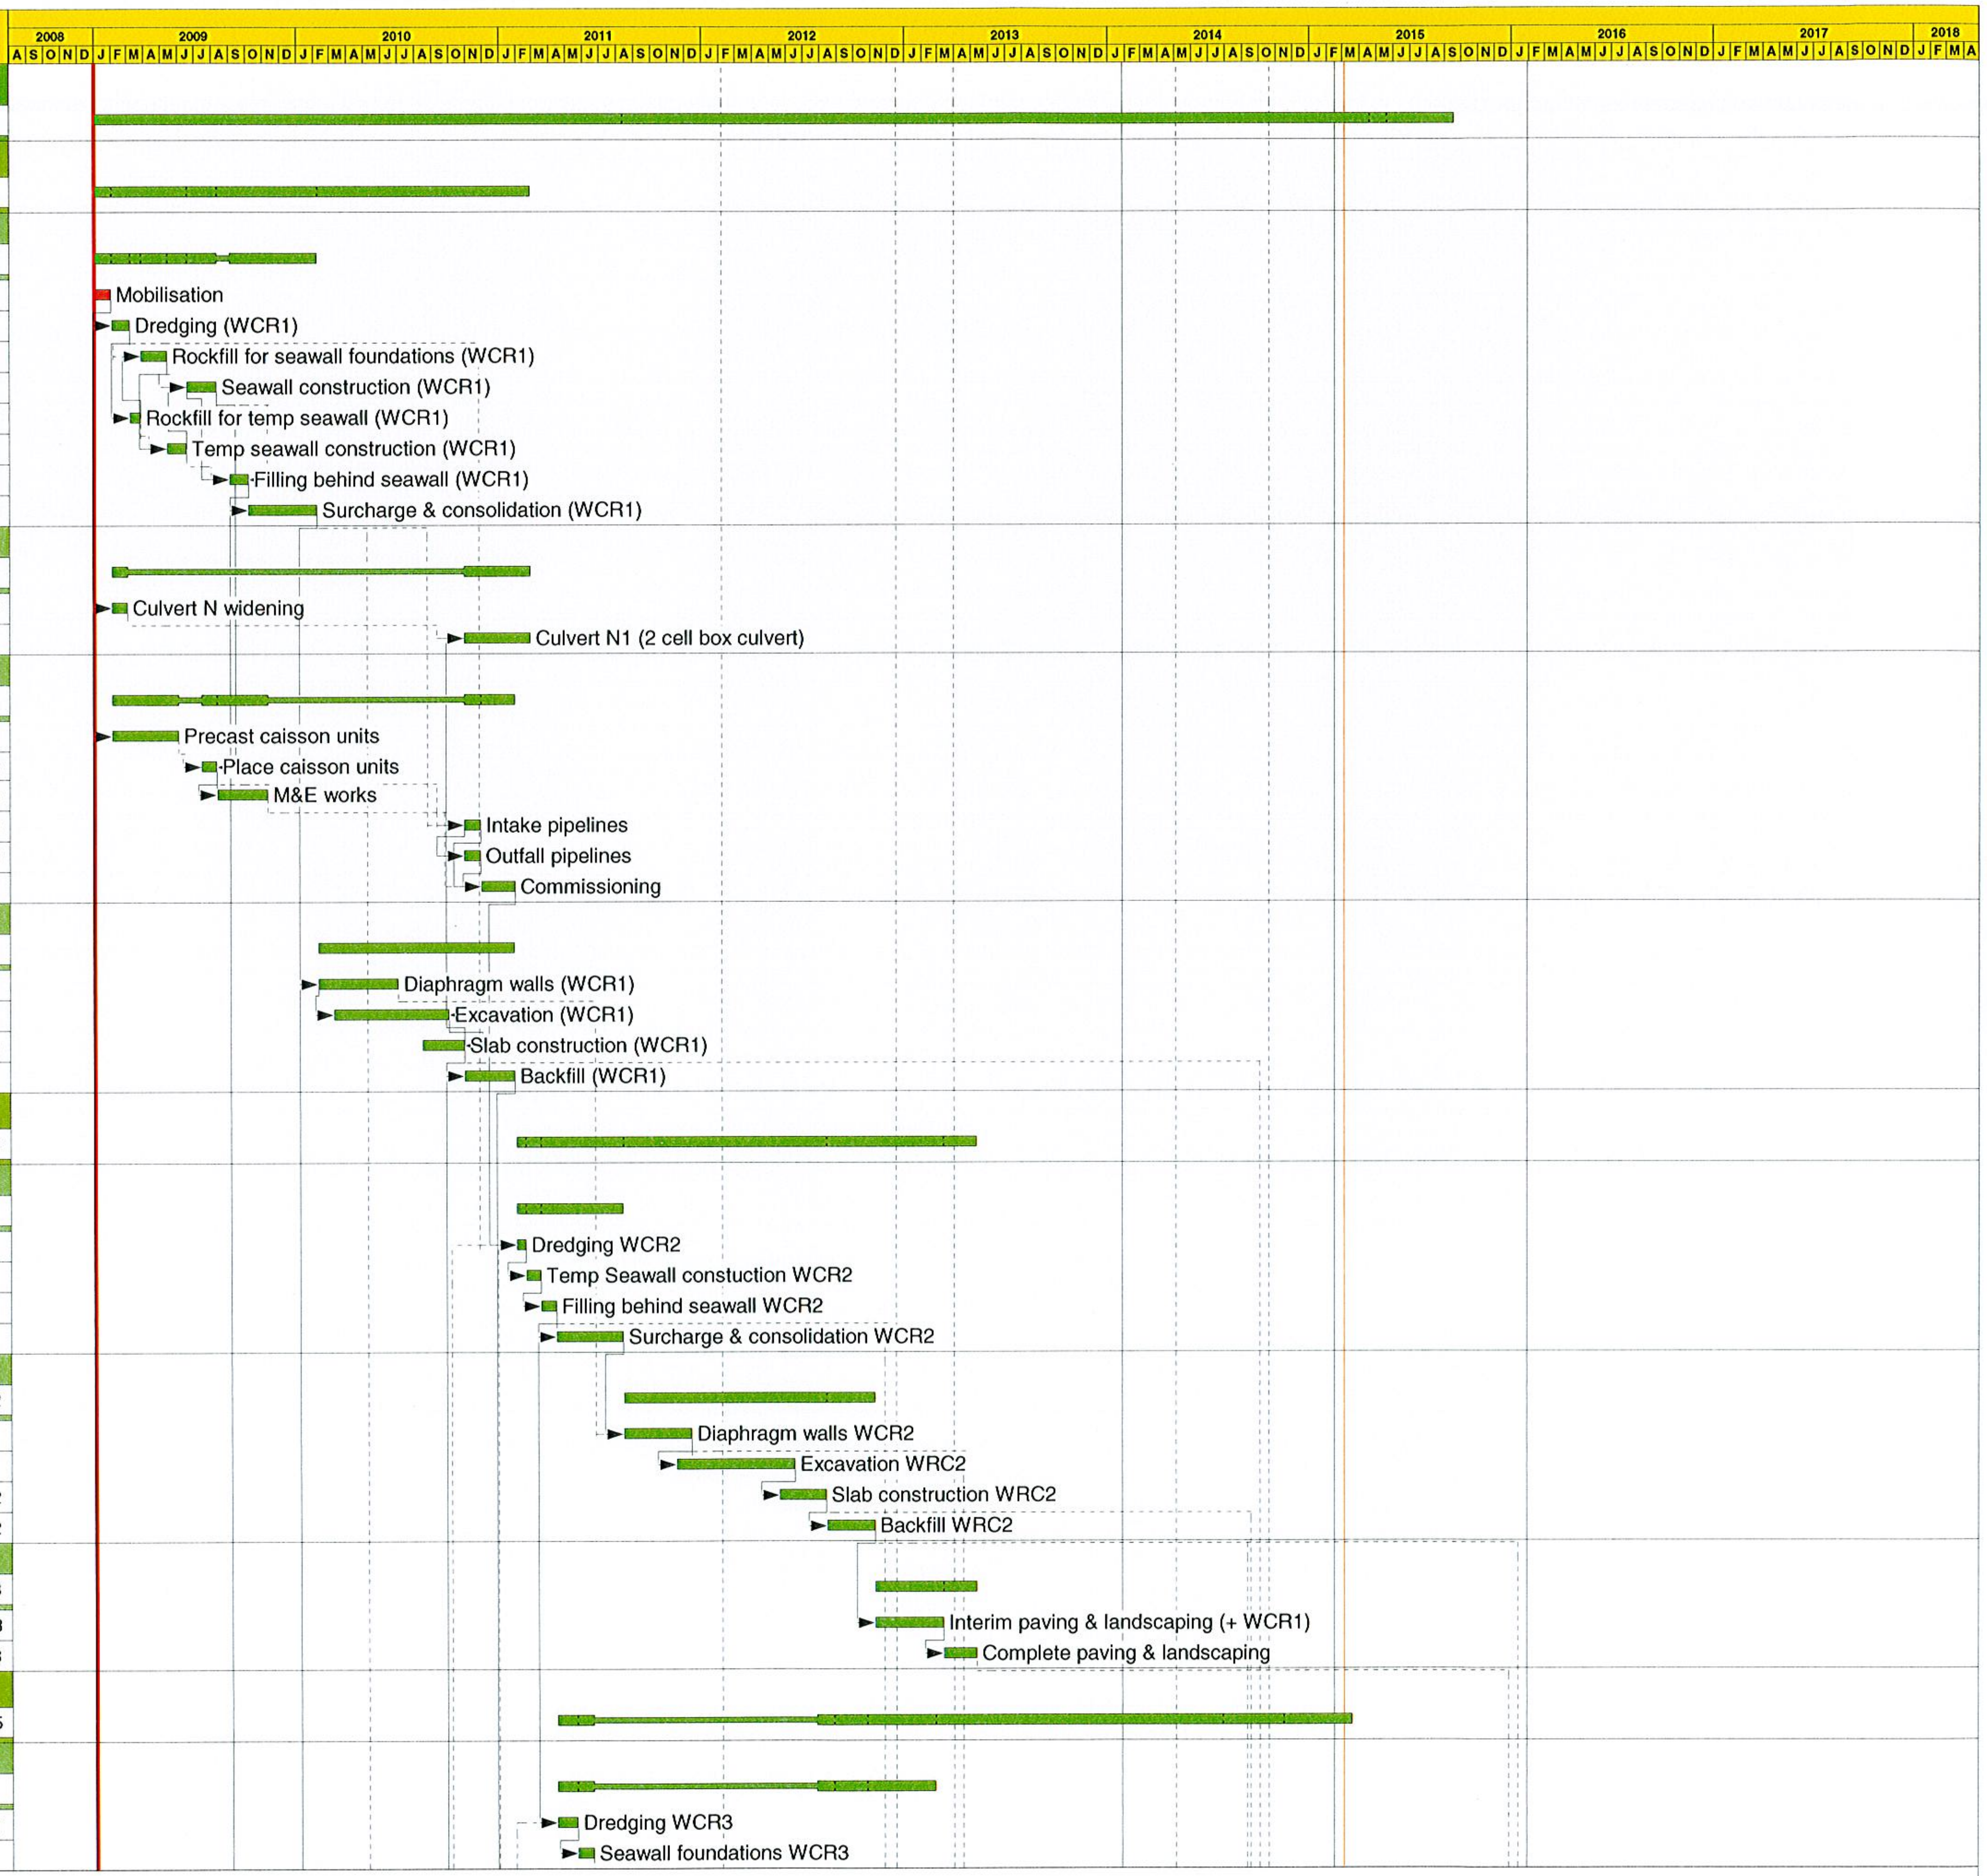

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	4A

Act ID	Description	Orig Dur	Early Start	Early Finish
331020	Seawall construction WCR3	28d	25JUL12	25AUG12
331030	Filling behind seawall WCR3	51d	27AUG12	24OCT12
331100	Surcharge & consolidation WCR3	104d	25OCT12	25FEB13
CWB Tunnel				
		537d	26FEB13	15NOV14
333000	Diaphragm walls WCR3	128d	26FEB13	24JUL13
333010	Excavation WCR3	252d	27JUN13	18APR14
333020	Slab construction WRC3	110d	22MAR14	28JUL14
333030	Backfill WCR3	95d	29JUL14	15NOV14
Promenade				
		104d	17NOV14	19MAR15
333040	Interim paving & landscaping	104d	17NOV14	19MAR15
3.4 Wan Chai Reclamation Stage 4				
		746d	25OCT12	20MAR15
Dredging, Filling & Seawall				
		190d	25OCT12	05JUN13
341000	Dredging WCR4	15d	25OCT12	10NOV12
341010	Seawall foundations WCR4	25d	12NOV12	10DEC12
341020	Seawall construction WCR4	28d	11DEC12	14JAN13
341030	Filling behind seawall WCR4	18d	15JAN13	04FEB13
341040	Surcharge & consolidation WCR4	104d	05FEB13	05JUN13
Drainage Culverts				
		660d	05FEB13	20MAR15
342000	Divert Culvert O through PCWA	52d	05FEB13	05APR13
342010	Demolish Culvert O over CWB	26d	07MAY13	05JUN13
342020	Reconstruct & widen Culvert O	125d	24JUN14	15NOV14
342040	Culvert O1 (3 cell box culvert)	105d	17NOV14	20MAR15
CWB Tunnel				
		414d	06JUN13	03OCT14
343000	Diaphragm walls WCR4	134d	06JUN13	08NOV13
343010	Excavation WCR4	190d	05OCT13	16MAY14
343020	Slab construction WCR4	62d	12APR14	23JUN14
343021	Reinstate culvert over tunnel WCR4	35d	14MAY14	23JUN14
343030	Backfill WCR4	88d	24JUN14	03OCT14
Promenade				
		104d	04OCT14	04FEB15
334000	Interim paving & landscaping	104d	04OCT14	04FEB15
3.6 Ferry Pier Reprovisioning				
		722d	02FEB09	27MAY11
Temporary Ferry Piers				
		52d	02FEB09	02APR09
361000	Preparation of temporary piers	52d	02FEB09	02APR09
361010	Relocation to temporary piers	0		02APR09
New Ferry Piers				
		670d	03APR09	27MAY11
362000	Piling & deck construction	208d	03APR09	01DEC09
362010	Superstructure & services	104d	02DEC09	03APR10
362020	Relocate WCE ferry piers	0		28JAN11
362030	Demolish existing pier structures	102d	29JAN11	27MAY11
3.7 Helipad Reprovisioning				
		460d	02JAN09	24JUN10
Reprovisioning at HKCEC				
		460d	02JAN09	24JUN10
372000	Deck construction & demolition	280d	02JAN09	24NOV09
372010	Helipad facilities	180d	25NOV09	24JUN10
372020	Relocate helipad	0		24JUN10

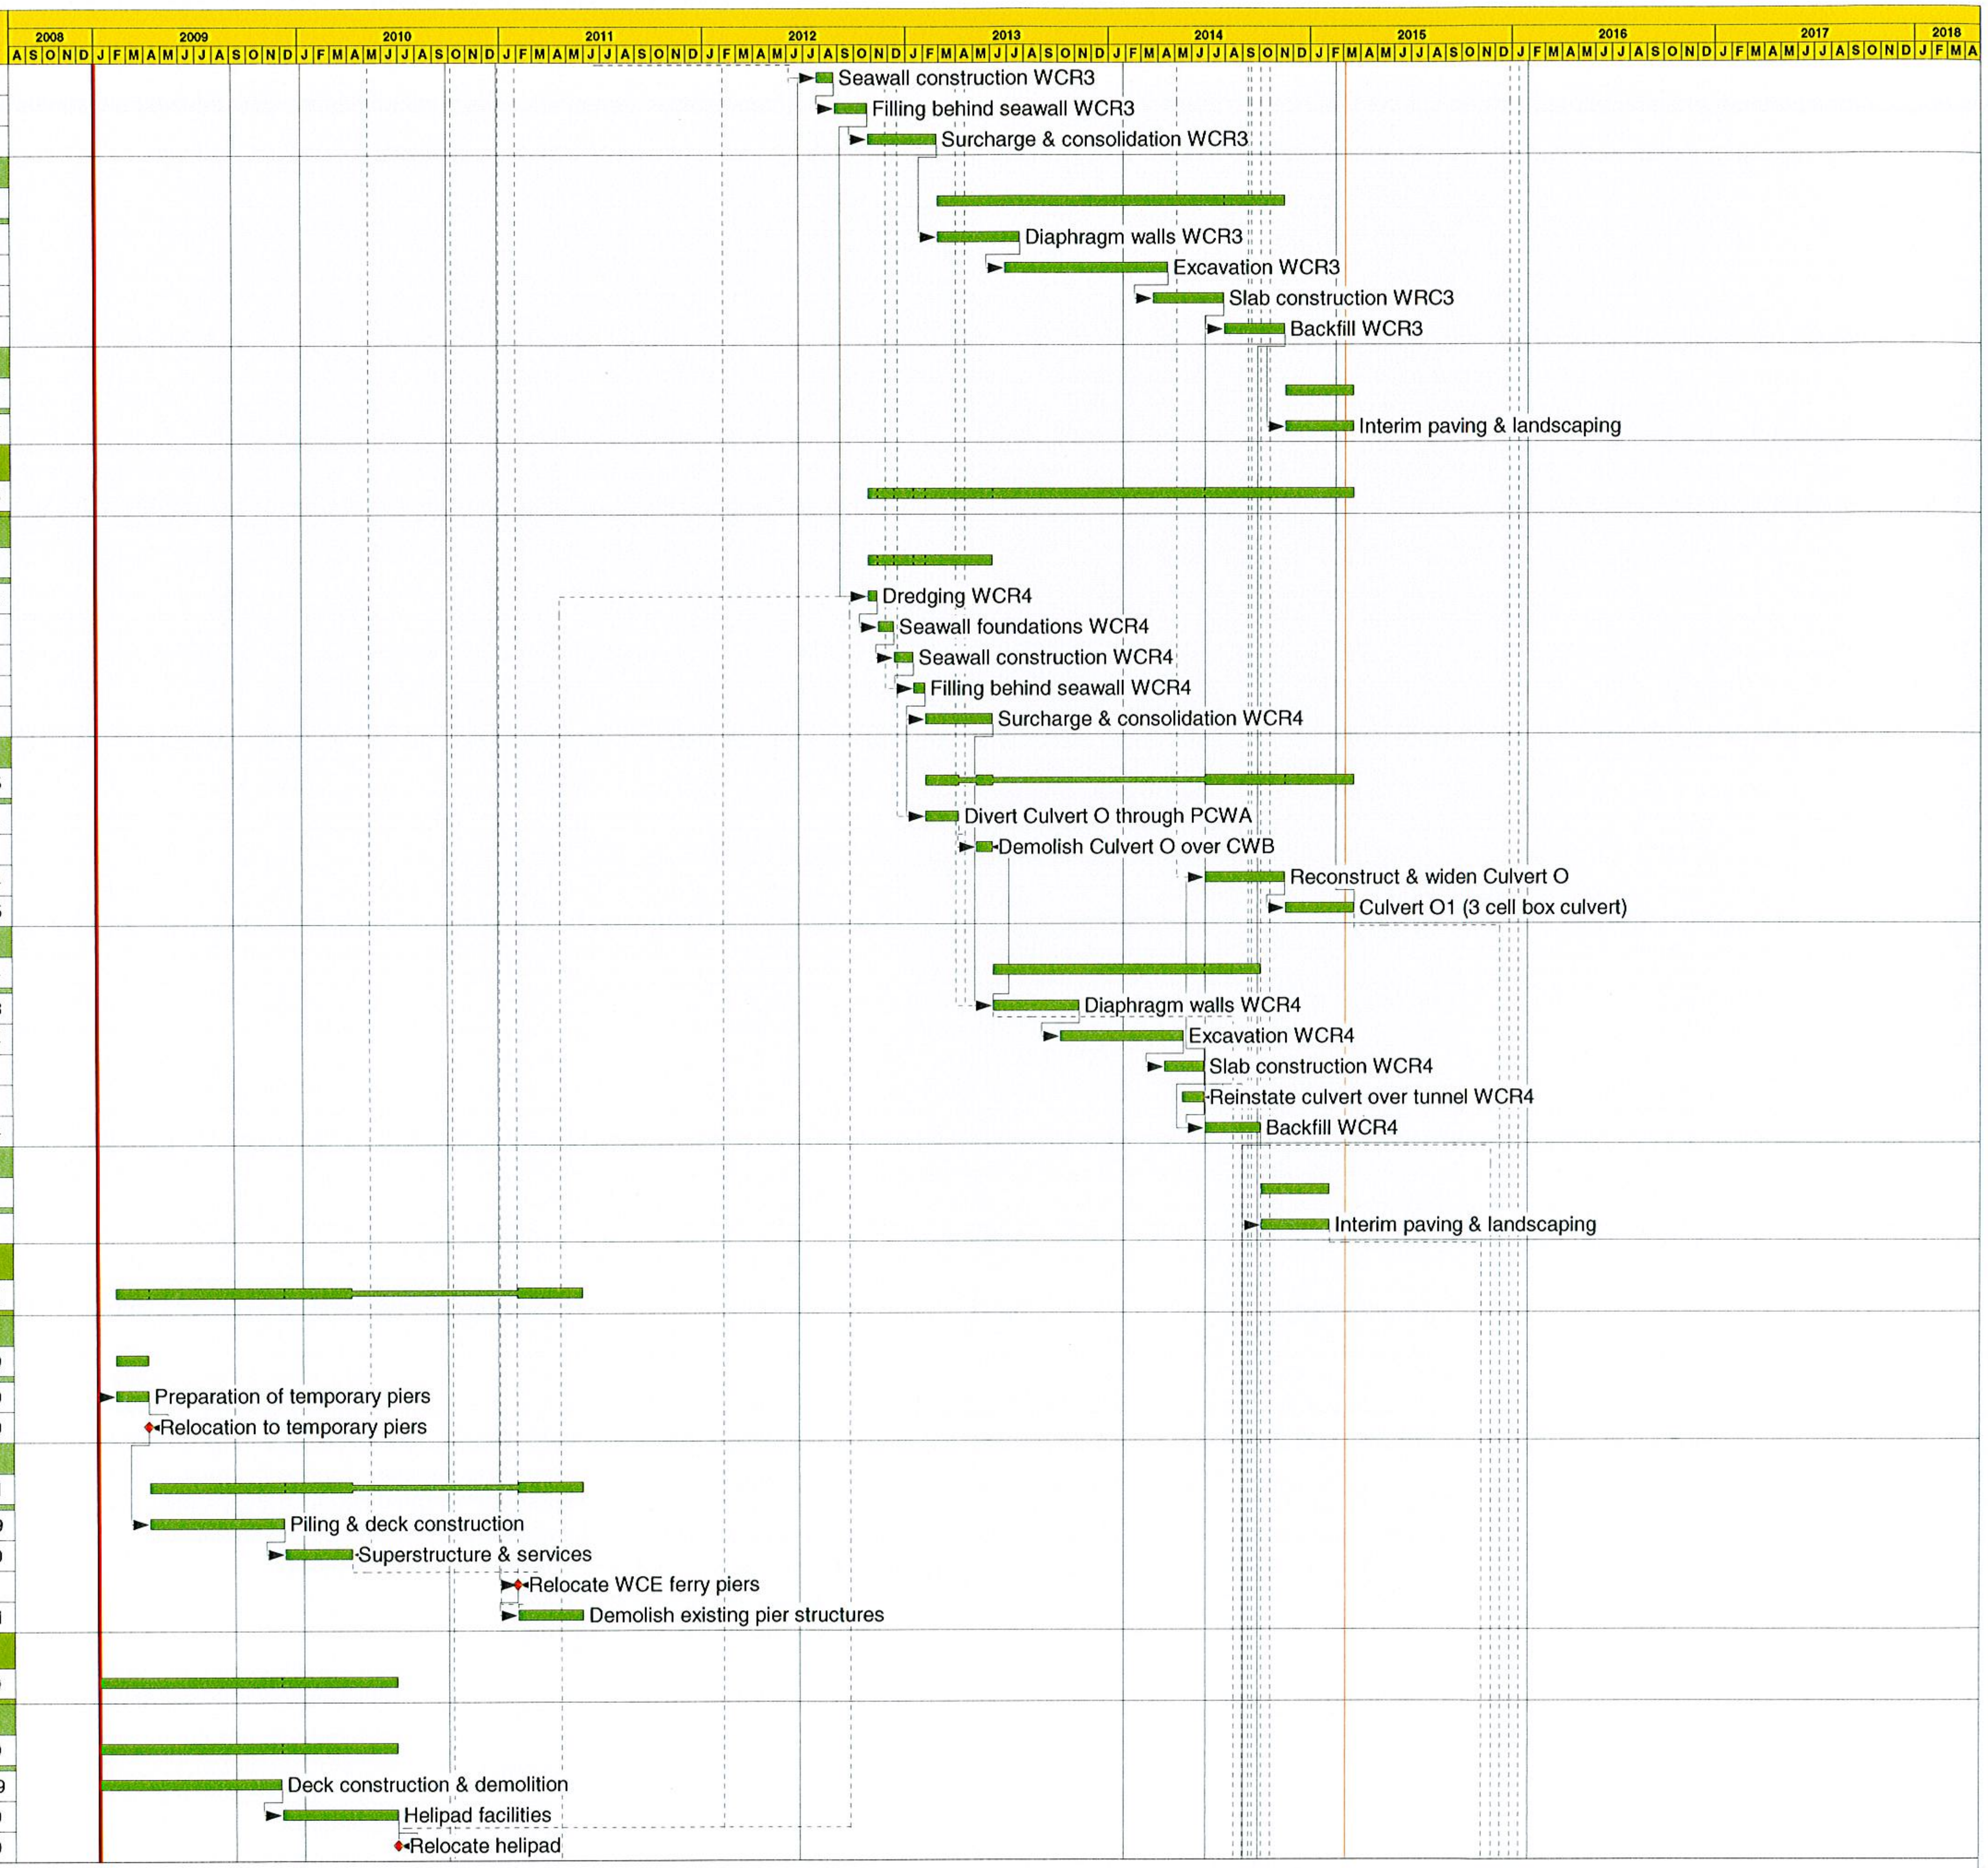

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	5A

Act ID	Description	Orig Dur	Early Start	Early Finish
3.8 Sewage Outfall				
		475d	07OCT09	16APR11
Marine Section				
		234d	07OCT09	07JUL10
381000	Submarine pipelines (2x1600dia)	234d	07OCT09	07JUL10
Land Section				
		144d	29OCT10	16APR11
382000	New 2250dia pipeline to WCESSP	118d	29OCT10	17MAR11
382010	Commissioning	26d	18MAR11	16APR11
3.9 WSD's Salt Water Pumping Station				
		522d	02FEB09	04OCT10
390000	Diversion of intake	90d	08FEB10	22MAY10
390010	Construct new pumping station	180d	02FEB09	29AUG09
390030	Connection back to existing system	64d	24MAY10	04AUG10
390040	M&E works	78d	31AUG09	28NOV09
390050	Commissioning	52d	05AUG10	04OCT10
3.10 Roads				
		297d	04OCT14	17SEP15
3101000	Road P2 from Fleming Rd to Marsh Rd	104d	17NOV14	19MAR15
3101010	Realign Hung Hing Road	156d	04OCT14	06APR15
3101030	Connection to Tonnochy Rd	26d	20MAR15	18APR15
3101040	Connection to Marsh Rd	26d	20APR15	19MAY15
3101050	Hung Hing Rd & RHKYC access	104d	20MAY15	17SEP15
3.11 Handover / Completion Dates				
		355d	28JUL14	17SEP15
3111010	Handover tunnel to HyD for CWB construction	0		28JUL14
3111020	Completion of WCR construction	0		17SEP15
4. HKCEC RECLAMATION				
		2259d	31DEC08	02APR16
4.1 HKCEC Reclamation Stage 1 (Water Channel)				
		2259d	02JAN09	02APR16
Dredging, Seawalls & Filling				
		96d	02JAN09	23APR09
411000	Mobilisation	26d	02JAN09	31JAN09
411010	Extract abandoned piles	52d	02FEB09	02APR09
411015	Dredging HKCEC1	14d	02FEB09	17FEB09
411020	Temp seawalls HKCEC1	38d	18FEB09	02APR09
411030	Filling behind seawalls HKCEC1	18d	03APR09	23APR09
Cooling Water Systems				
		1955d	23DEC09	02APR16
412000	Intake pipelines (HKCEC West)	200d	23DEC09	13AUG10
412020	M&E works (HKCEC)	104d	14AUG10	13DEC10
412030	Commissioning (HKCEC)	104d	14DEC10	15APR11
412050	Outfall pipelines along Expo Drive East	240d	26JUN15	02APR16
CWB Tunnel				
		208d	24APR09	22DEC09
413000	Diaphragm walls HKCEC1	60d	24APR09	02JUL09
413005	NHKIL diaphragm wall HKCEC1	30d	03JUL09	06AUG09
413010	Excavation HKCEC1	82d	22MAY09	25AUG09
413015	NHKIL excavation HKCEC1	54d	26AUG09	27OCT09
413020	Slab construction HKCEC1	56d	20JUL09	22SEP09
413025	NHKIL slab construction HKCEC1	37d	28OCT09	09DEC09
413030	Backfill HKCEC1	17d	23SEP09	12OCT09
413035	NHKIL backfill HKCEC1	11d	10DEC09	22DEC09

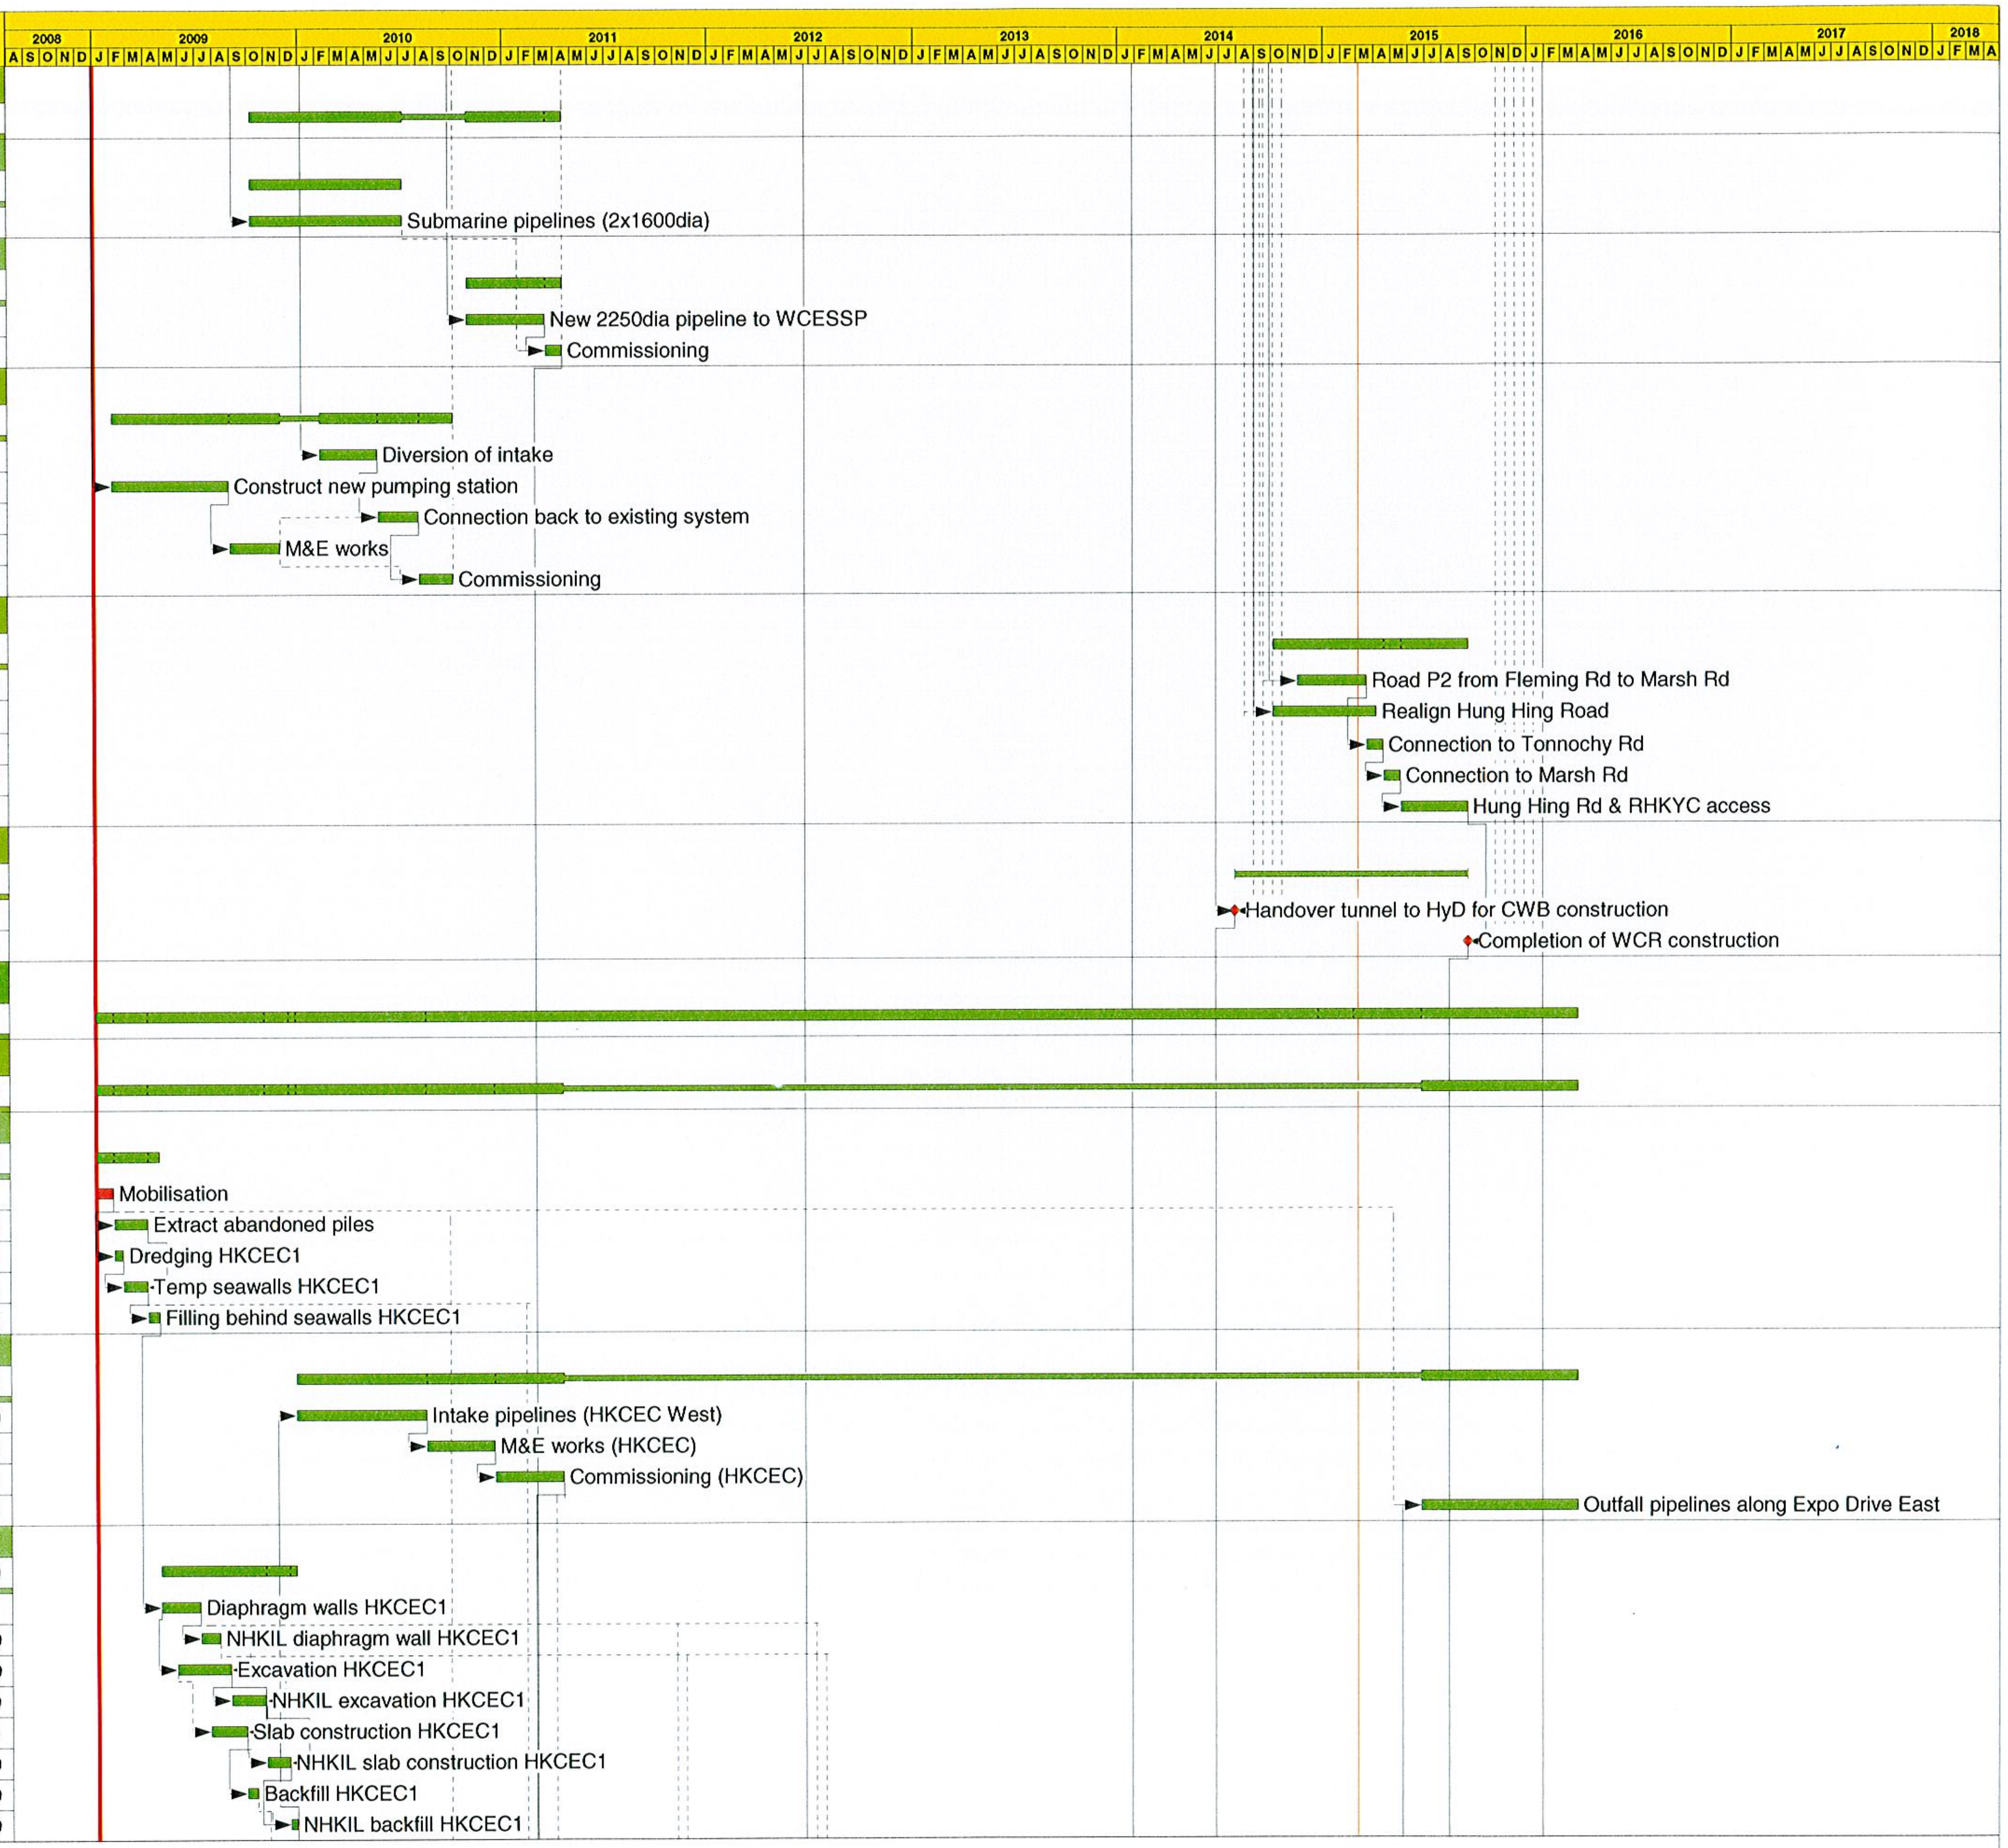

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	6A

Act ID	Description	Orig Dur	Early Start	Early Finish
4.2 HKCEC Reclamation Stage 2				
		1634d	31DEC08	31MAR14
Dredging, Seawalls & Filling				
		1170d	31DEC08	01OCT12
421000	CRIII completion of Reclamation FRAE	0		31DEC08
421010	Divert services & road access	104d	23DEC09	24APR10
421020	Demolish west bridge	40d	26APR10	10JUN10
421030	Dredging HKCEC2E	34d	08JUN11	16JUL11
421040	Seawall foundations HKCEC2E	31d	18JUL11	22AUG11
421050	Seawall construction HKCEC2E	30d	16JAN12	18FEB12
421060	Filling behind seawall HKCEC2E	55d	10MAR12	12MAY12
421070	Surcharge & consolidation	104d	14MAY12	11SEP12
421080	Dredging HKCEC2W	44d	18APR11	07JUN11
421090	Seawall foundations HKCEC2W	39d	08JUN11	22JUL11
421100	Seawall construction HKCEC2W	38d	02DEC11	14JAN12
421110	Filling behind seawall HKCEC2W	72d	10MAR12	01JUN12
421120	Surcharge & consolidation	104d	02JUN12	01OCT12
Drainage Culverts				
		240d	22JUN13	31MAR14
422000	Culvert L widening	64d	22JUN13	04SEP13
422010	Culvert L1 (2 cell box culvert)	176d	05SEP13	31MAR14
CWB Tunnel				
		459d	01OCT12	25MAR14
424000	CRIII completion of CWB tunnel box (FRAE)	0		01OCT12
424010	Diaphragm walls (HKCEC2E)	112d	11JUL13	18NOV13
424015	NHKIL diaphragm wall	50d	19NOV13	17JAN14
424020	Excavation (HKCEC2E)	69d	27SEP13	16DEC13
424025	NHKIL excavation	46d	21DEC13	14FEB14
424030	Slab construction (HKCEC2E)	48d	19NOV13	15JAN14
424035	NHKIL slab construction	32d	06FEB14	14MAR14
424040	Backfill (HKCEC2E)	14d	16JAN14	31JAN14
424045	NHKIL backfill	9d	15MAR14	25MAR14
424050	Diaphragm walls (HKCEC2W)	160d	02OCT12	08APR13
424055	NHKIL diaphragm wall	80d	09APR13	10JUL13
424060	Excavation (HKCEC2W)	88d	24JAN13	06MAY13
424065	NHKIL excavation	46d	15JUN13	07AUG13
424070	Slab construction (HKCEC2W)	61d	25MAR13	03JUN13
424075	NHKIL slab construction	32d	30JUL13	04SEP13
424080	Backfill (HKCEC2W)	19d	04JUN13	25JUN13
424085	NHKIL backfill	9d	05SEP13	14SEP13
4.3 MTR Tunnel Crossing				
		404d	29OCT10	14FEB12
Piling				
		144d	29OCT10	16APR11
431000	Piling for tunnel units	92d	29OCT10	15FEB11
431010	Piling for deck	52d	16FEB11	16APR11
Tunnel & Deck Construction				
		364d	15DEC10	14FEB12
433000	Precast & place CWB tunnel unit	130d	17AUG11	14JAN12
433005	Precast & place NIL tunnel unit	104d	15DEC10	16APR11
433006	Precast & place deck units	104d	18APR11	16AUG11
433020	Seawall construction	26d	16JAN12	14FEB12

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	7A

Act ID	Description	Orig Dur	Early Start	Early Finish
4.4 HKCEC Reclamation Stage 3				
		1411d	30MAR09	07OCT13
Dredging, Seawalls & Filling				
		867d	30MAR09	09JAN12
441000	Demolition of Temp Bridge under Atrium Link	0		30MAR09
441005	Dredging HKCEC3	23d	21MAR11	15APR11
441010	Temp seawall HKCEC3W	26d	16APR11	16MAY11
441020	Filling HKCEC3W	20d	17MAY11	08JUN11
441030	Divert road & services on HKCEC3W	104d	09JUN11	07OCT11
441040	Demolish east bridge	40d	08OCT11	23NOV11
441050	Filling HKCEC3E to culvert invert level	40d	24NOV11	09JAN12
Drainage Culverts				
		227d	03NOV11	24JUL12
442000	Culvert M widening	58d	03NOV11	09JAN12
442020	2 cell box culvert (M2a)	92d	10JAN12	25APR12
442030	3 cell box culvert (M2a/b)	94d	06APR12	24JUL12
CWB Tunnel				
		544d	10JAN12	07OCT13
443000	Diaphragm walls HKCEC3Ea	30d	10JAN12	13FEB12
443010	Excavation HKCEC3Ea	41d	14FEB12	31MAR12
443020	Slab construction HKCEC3Ea	28d	02APR12	03MAY12
443030	Backfill HKCEC3Ea	8d	04MAY12	12MAY12
443035	Divert road & services on HKCEC3Ea	104d	25JUL12	22NOV12
443040	Diaphragm walls HKCEC3W&Eb	93d	23NOV12	13MAR13
443045	NHKIL diaphragm wall HKCEC3	45d	14MAR13	04MAY13
443050	Excavation HKCEC3W&Eb	135d	21DEC12	29MAY13
443055	NHKIL excavation HKCEC3	70d	30MAY13	19AUG13
443060	Slab construction HKCEC3W&Eb	80d	26MAR13	26JUN13
443065	NHKIL slab construction HKCEC3	50d	20JUL13	16SEP13
443070	Backfill HKCEC3W&Eb	44d	27JUN13	16AUG13
443075	NHKIL backfill HKCEC3	18d	17SEP13	07OCT13
4.5 Roads				
		520d	26MAR14	24NOV15
451000	Road P2 from CRIII to Fleming Rd	234d	26MAR14	23DEC14
451020	Expo Drive & slip roads	104d	25FEB15	25JUN15
451030	Expo Drive East	78d	26JUN15	24SEP15
451040	Connection to Fenwick Pier Str	52d	24DEC14	24FEB15
451050	Connection to Fleming Rd	52d	25SEP15	24NOV15
451060	Extend PTI	52d	27JUL15	24SEP15
4.6 Handover / Completion Dates				
		579d	15JAN14	24NOV15
461000	Handover tunnel to HyD for CWB construction	0		15JAN14
461010	Completion of HKCEC construction	0		24NOV15
5. CROSS HARBOUR WATERMAINS				
		538d	02JAN09	22SEP10
5.1 Submarine Pipeline				
		538d	02JAN09	22SEP10
511000	Mobilisation & procurement	104d	02JAN09	02MAY09
511020	Lay new submarine pipeline	330d	04MAY09	25MAY10
511030	Connection to TST watermains	52d	26MAY10	23JUL10
511040	Connection to Wan Chai watermains	52d	26MAY10	23JUL10
511060	Commissioning	52d	24JUL10	22SEP10
5.2 Land Sections				
		217d	12SEP09	25MAY10
521000	TST landfall	87d	13FEB10	25MAY10
521010	Lay land pipelines HKCEC	217d	12SEP09	25MAY10

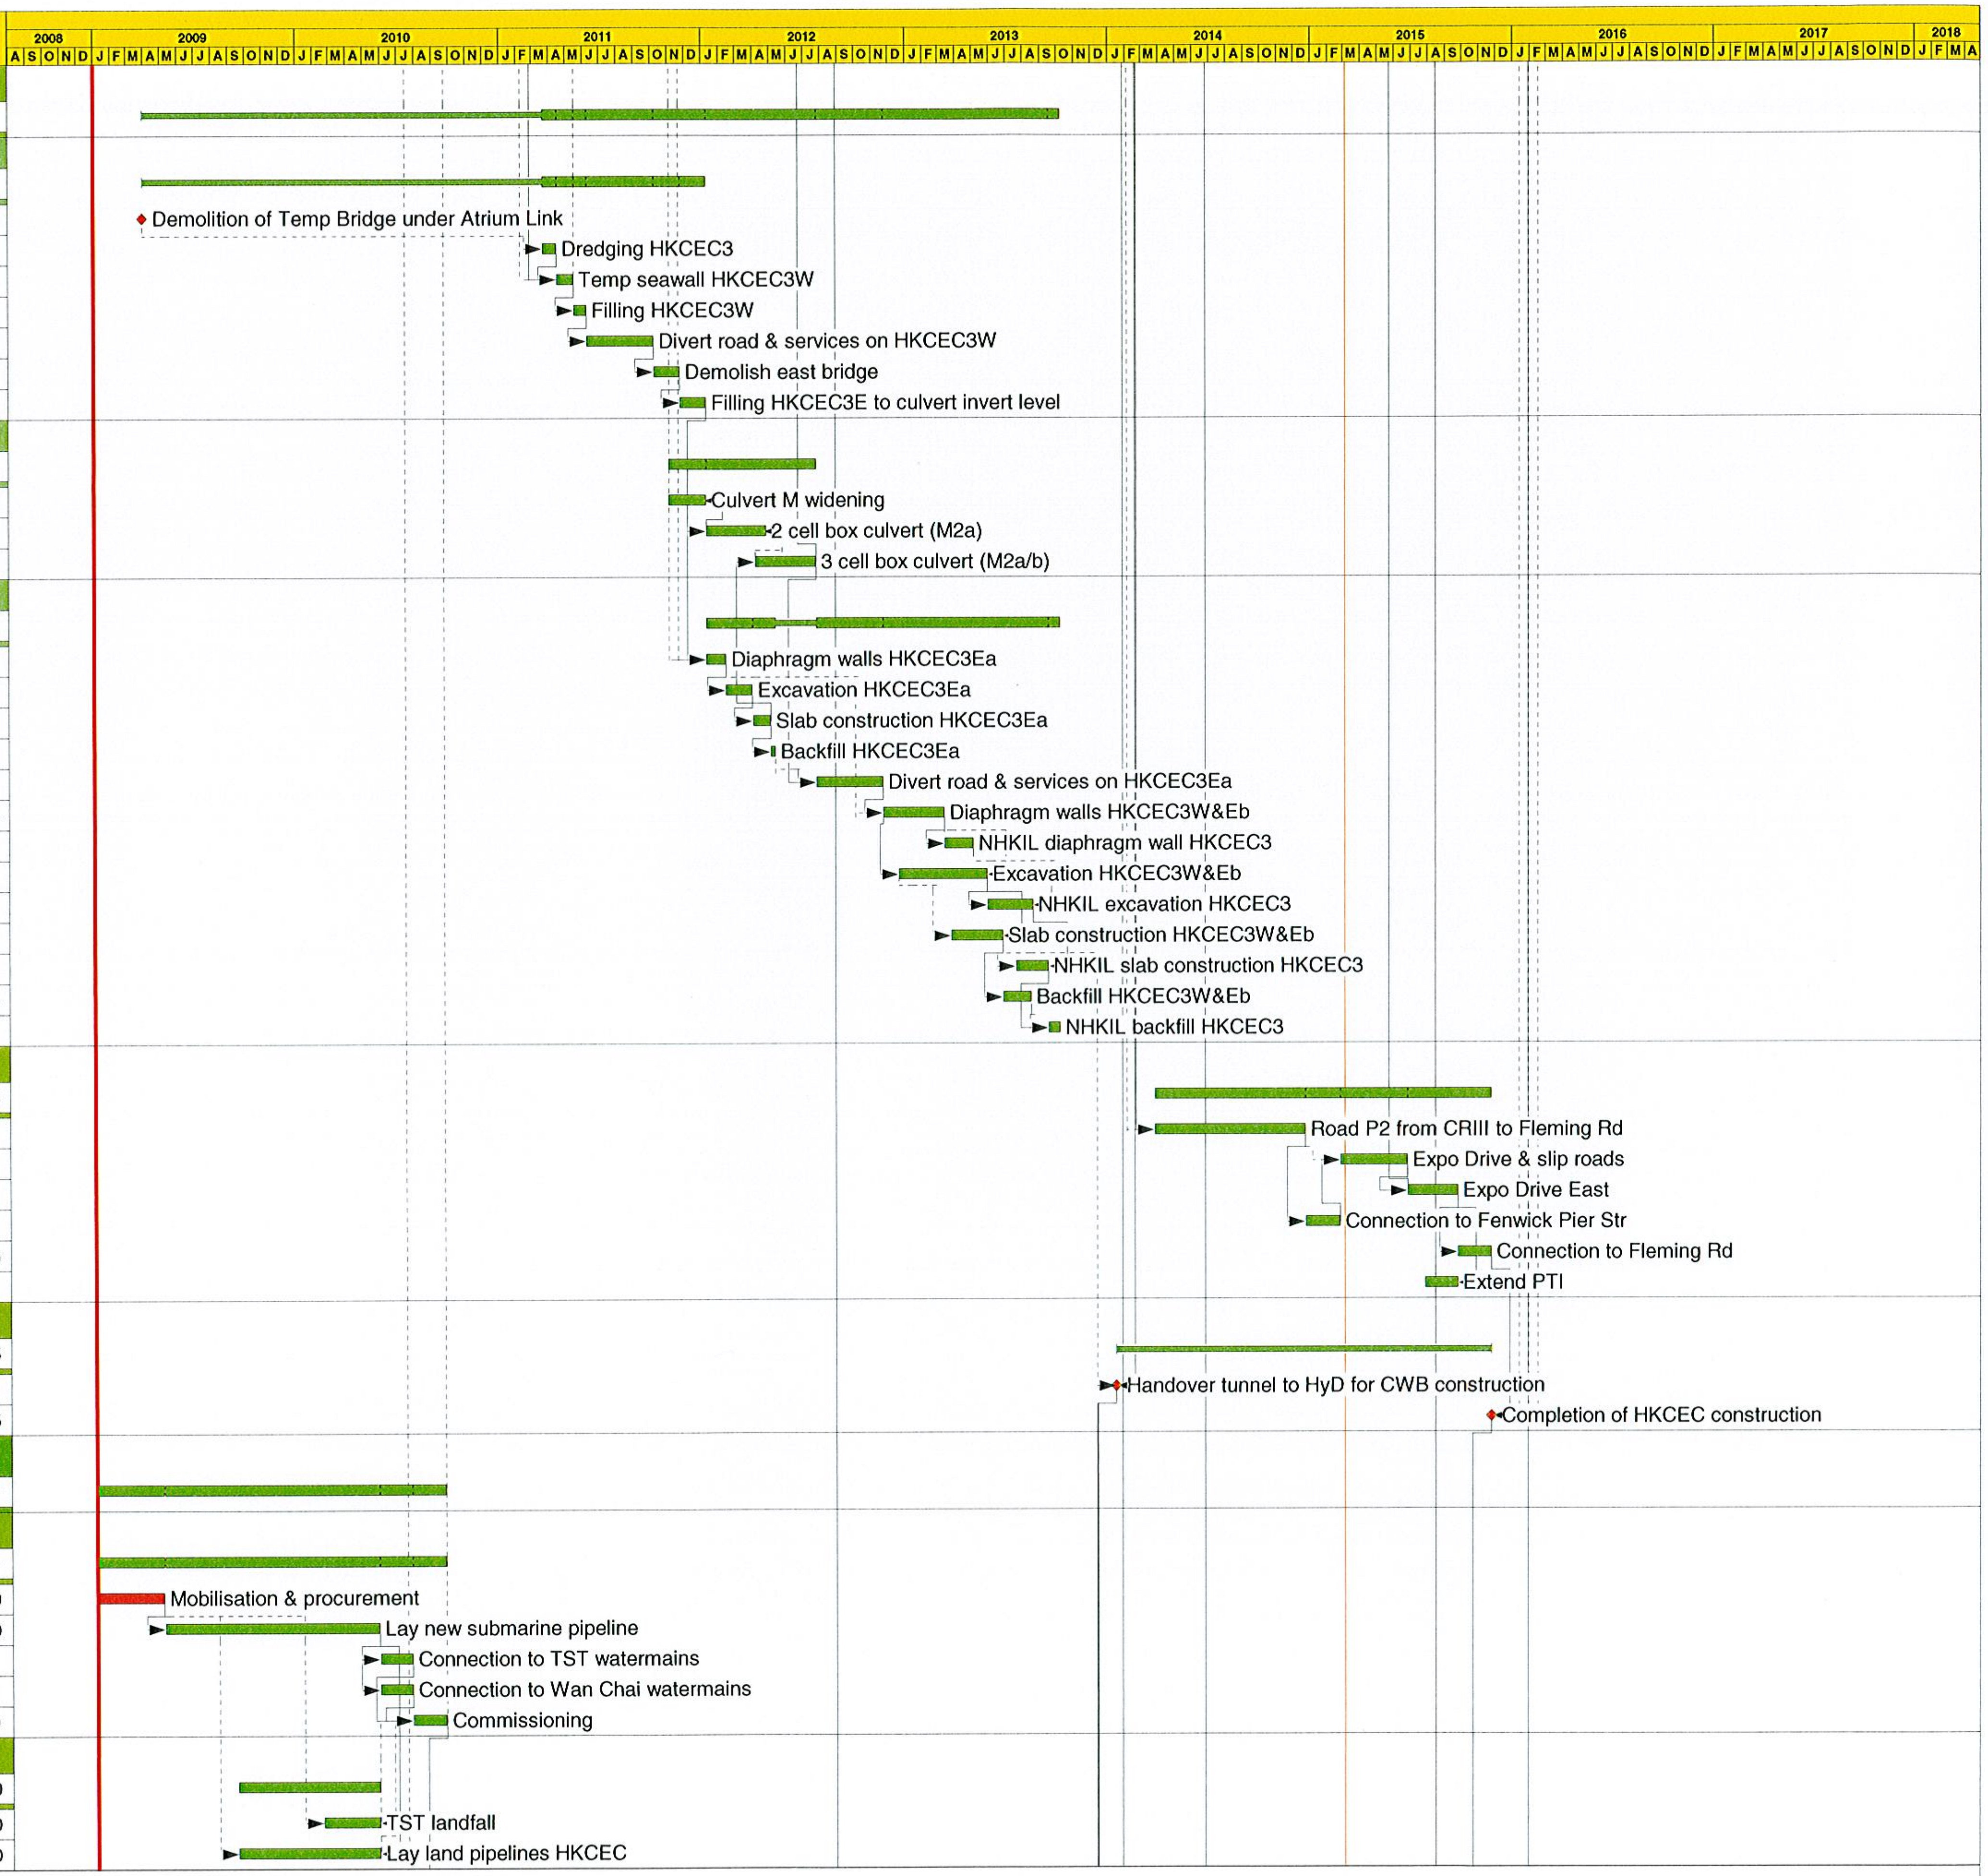

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	8A

Act ID	Description	Orig Dur	Early Start	Early Finish
6. NORTH POINT RECLAMATION				
		2481d	02JAN09	17DEC16
6.1 North Point Reclamation Stage 1				
		546d	02JAN09	01OCT10
Dredging, Seawall & Filling				
		318d	02JAN09	09JAN10
610000	Mobolization	26d	02JAN09	31JAN09
611000	Dredging NPR1	31d	02FEB09	09MAR09
611010	Rockfill for Seawall NPR1	47d	10MAR09	02MAY09
611020	Seawall Construction NPR1	70d	04MAY09	23JUL09
611030	Filling behind seawall NPR1	40d	24JUL09	08SEP09
611040	Surcharge & Consolidation NPR1	104d	09SEP09	09JAN10
CWB Tunnel NPR1				
		228d	11JAN10	01OCT10
612010	Diaphragm Wall NPR1	95d	11JAN10	30APR10
612020	Excavation NPR1	61d	01MAY10	09JUL10
612030	Slab Construction NPR1	58d	10JUL10	15SEP10
612040	Backfilling NPR1	14d	16SEP10	01OCT10
612050	Handover NPR1 for IECL construction	0		01OCT10
6.2 North Point Reclamation Stage 2				
		1110d	14APR09	01NOV12
Dredging, Seawall & Filling (NPR2E)				
		467d	11MAY09	06NOV10
621000	Dredging NPR2E	73d	11MAY09	03AUG09
621010	Rockfill for Seawall NPR2E	77d	04AUG09	31OCT09
621020	Seawall Construction NPR2E	116d	02NOV09	18MAR10
621030	Filling behind seawall NPR2E	97d	19MAR10	08JUL10
621040	Surcharge & Consolidation NPR2E	104d	09JUL10	06NOV10
622050	Handover NPR2E for IECL construction	0		06NOV10
Dredging, Seawall & Filling (NPR2W)				
		228d	14APR09	06JAN10
621050	Dredging NPR2W	23d	14APR09	09MAY09
621060	Rockfill for Seawall NPR2W	29d	11MAY09	12JUN09
621070	Seawall Construction NPR2W	44d	13JUN09	03AUG09
621080	Filling behind seawall NPR2W	28d	04AUG09	04SEP09
621090	Surcharge & Consolidation NPR2W	104d	05SEP09	06JAN10
CWB Tunnel (NPR2W)				
		882d	07JAN10	01NOV12
623010	Diaphragm Wall NPR2W (Outside FHED Depot)	33d	07JAN10	13FEB10
623060	Diaphragm Wall NPR2W (within FHED Depot)	80d	20JAN12	21APR12
623065	Foundation of East Ventilation Bldg	80d	20JAN12	21APR12
623070	Excavation NPR2W	98d	23APR12	14AUG12
623080	Slab Construction NPR2W	48d	15AUG12	09OCT12
623090	Backfilling NPR2W	20d	10OCT12	01NOV12
6.3 Promenade				
		100d	24AUG16	17DEC16
640000	Promenade (NP) Final	100d	24AUG16	17DEC16
6.4 Handover / Completion Dates				
		1284d	01NOV12	17DEC16
650000	Handover CWB Tunnel to HyD	0		01NOV12
650010	Completion of NP Reclamation	0		17DEC16

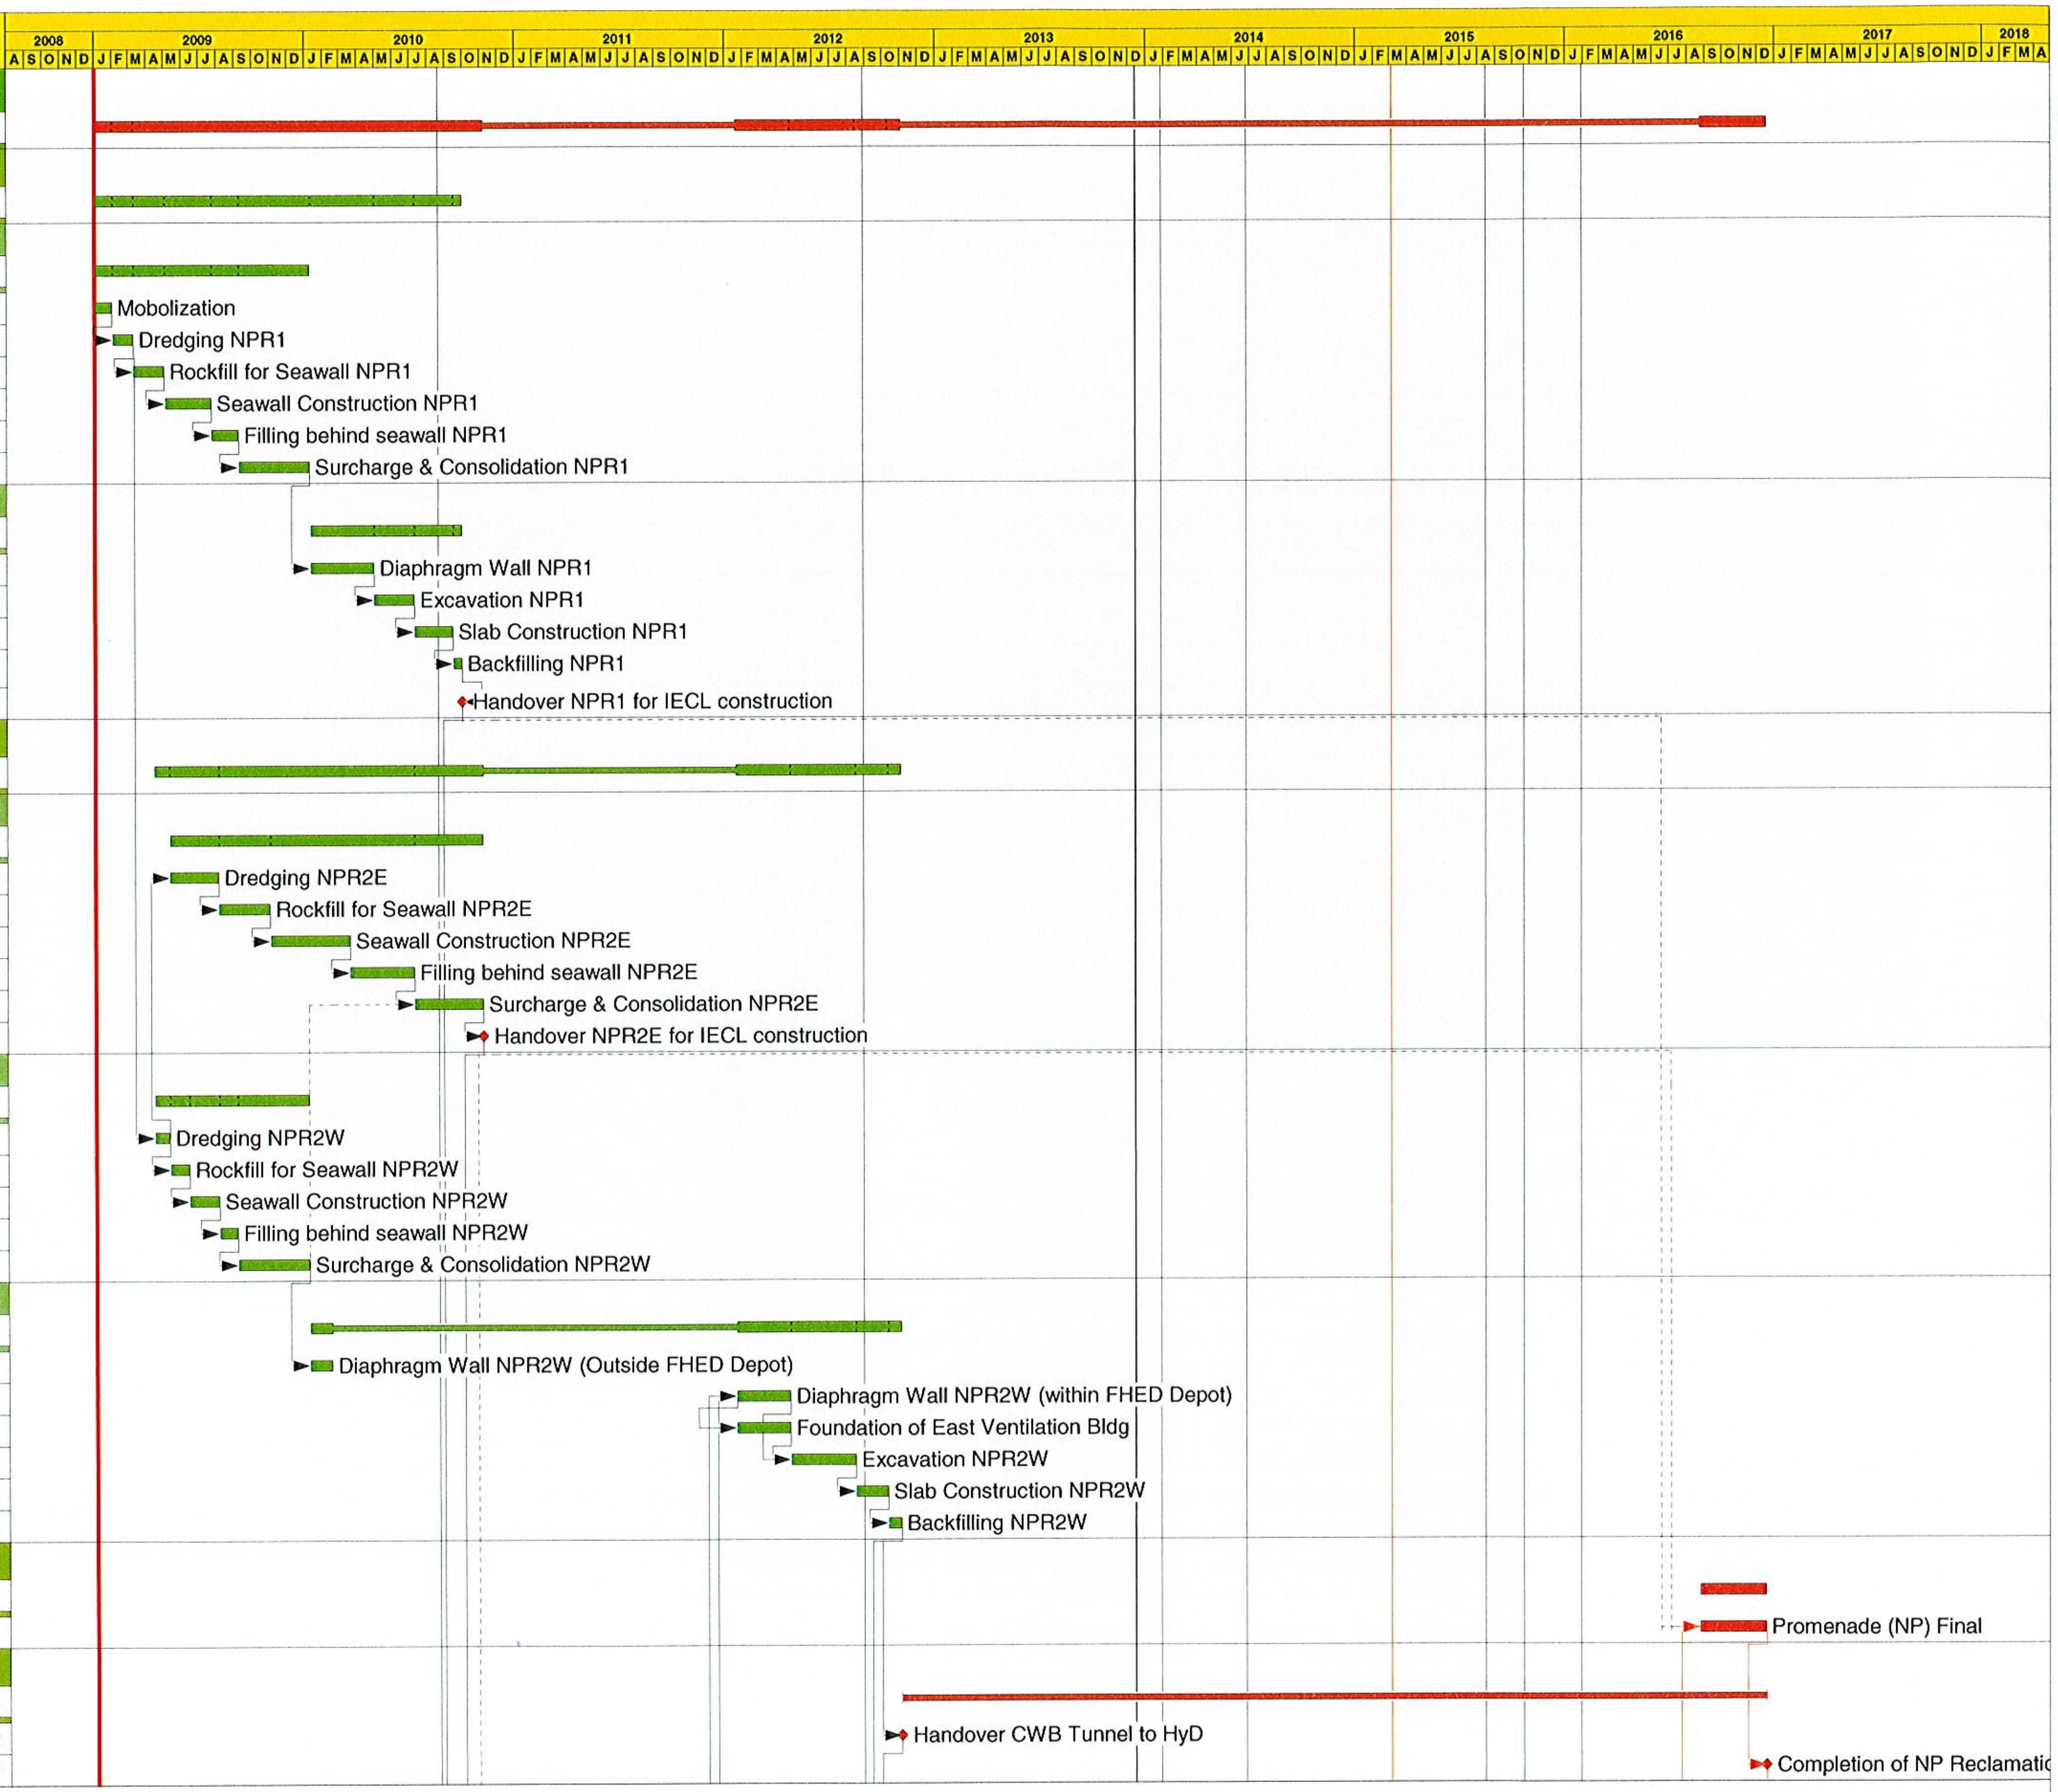

Maunsell

Agreement No. CE 54/2001
Wan Chai Development Phase II - Design & Construction

CONSTRUCTION PROGRAMME

Project name	WDII_Oct08F
Data date	01JAN09
Run date	21NOV07
Page number	9A

Act ID	Description	Orig Dur	Early Start	Early Finish
7. Construction of IECL				
		1835d	02OCT10	23AUG16
7.2 IEC Connection Work				
		1745d	02OCT10	10MAY16
IEC E/B (HFS to Mainline)				
		731d	02OCT10	05FEB13
721010	Substructures (IECL E/B at NPR1)	65d	02OCT10	16DEC10
721040	Superstructure (IECL E/B at NPR1 w/ Temp Bridge)	180d	17DEC10	16JUL11
721050	Substructure (IECL E/B at NPR2E)	90d	17DEC10	02APR11
721060	Superstructure (IECL E/B at NPR2E w/Temp Bridge)	300d	04APR11	17MAR12
721070	Substructure (IECL E/B at NPR2W)	45d	20JAN12	12MAR12
721080	Superstructure (IECL E/B at NPR2W w/Temp	80d	02NOV12	05FEB13
721090	Handover NPR1 for Reprovision of FEHD Depot	0		16JUL11
721100	Handover FEHD Depot for Construction of IECL	0		19JAN12
IEC East Bound Traffic Diversion				
		15d	06FEB13	22FEB13
725010	Divert IEC E/B traffic to IECL E/B & Temp Bridge	15d	06FEB13	22FEB13
725020	Divert IEC W/B traffic to exist. IEC E/B	15d	06FEB13	22FEB13
Reconstruction IEC West Bound				
		620d	06FEB13	03FEB15
727020	Demolish IEC W/B	135d	06FEB13	12JUL13
727030	Substructure of Reconstructed IEC W/B	85d	17APR13	24JUL13
727050	Superstructure of Reconstructed IEC W/B	475d	25JUL13	03FEB15
IEC West Bound Traffic Diversion				
		14d	04FEB15	19FEB15
727060	Divert IEC W/B traffic to Reconstructed IEC W/B	14d	04FEB15	19FEB15
Mainline connection to IEC				
		380d	20FEB15	10MAY16
727110	Demolish IEC E/B for Connection to Trunk Road	60d	20FEB15	30APR15
727120	Substructure of IECL connection to Trunk Road	50d	01MAY15	27JUN15
727140	Superstructure of IECL connection to Trunk Road	270d	29JUN15	10MAY16
7.3 East Portal and IEC Connection				
		410d	01MAY15	23AUG16
Portal Construction				
		160d	01MAY15	03NOV15
731010	Substructure of Mainline East Portal	60d	01MAY15	09JUL15
731020	Retaining Structures of East Portal	100d	10JUL15	03NOV15
Traffic Diversion IEC E/B				
		74d	30MAY16	23AUG16
731030	Divert E/B Traffic to Trunk Road Tunnel	14d	30MAY16	14JUN16
731040	Demolish Temp. Bridge	60d	15JUN16	23AUG16
Handover Dates				
		74d	28MAY16	23AUG16
740000	Road Opening for Trunk Road	0		28MAY16
740010	Completion of IECL Construction	0		23AUG16
